



## Format "C"

Geotagged Photograph (JPG format) with details

Template enclosed

	S.No.	1
	Name of the work / project with location	Construction of Guard Room at Pologround Srinagar
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Srinagar
	AA Cost (Rs in lakhs)	Rs.6.00 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs.3,55,500/-
	Date of Start (Month / Year)	Oct. 2021
	Date of Completion (Month / Year)	March 2022
	No` . of Beneficiaries.	2

	S.No.	2
	Name of the work / project with location	Upgradation / Renovation of play field at Zindshah Masjid Rainawari Srinagar
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Srinagar
	AA Cost (Rs in lakhs)	36.00 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs.13,81,941/-
	Date of Start (Month / Year)	March 2022
	Date of Completion (Month / Year)	March 2022
	No` . of Beneficiaries.	2000



**With brief description of the project.**

S.No.	3
Name of the work / project with location	Providing and fixing of ACP hoardings for fencing of TRC ground Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	20.00 lacs
Total Cost of completion / Expenditure ending 3/2022	9,39,400/=
Date of Start (Month / Year)	Aug, 2021
Date of Completion (Month / Year)	March 2022
No` . of Beneficiaries.	1000



S.No.	4
Name of the work / project with location	Construction of Garage for departmental vehicles at Pologround Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	10.00 lacs
Total Cost of completion / Expenditure ending 3/2022	6,00,615/-
Date of Start (Month / Year)	Aug, 2021
Date of Completion (Month / Year)	March,2022
No` . of Beneficiaries.	500

### Geo-Tagged Photograph

1)



S.No.

5

Name of the work / project with location

Upgradation of Cricket ground at TRC Srinagar

Department /organization

YSS/ J&K Sports Council

Executing Agency

Executive Engineer J&K Sports Council, Srinagar

Block/ District

Srinagar

AA Cost (Rs in lakhs)

15.00 lacs

Total Cost of completion / Expenditure ending 3/2022

15.00 lacs

Date of Start (Month / Year)

11/08/2021

Date of Completion (Month / Year)


March 2022

No` . of Beneficiaries.

1000

### Geo-Tagged Photograph

1)

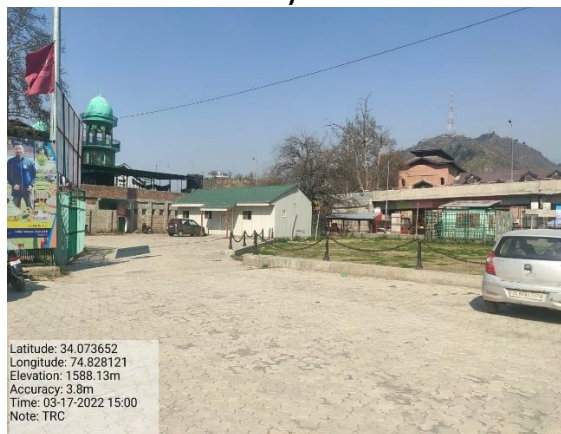

S.No.

6

Name of the work / project with location

Balance portion of chain and cast Iron pot with Ship Chain for Landscape area at TRC Football ground Srinagar

Department /organization

YSS/ J&K Sports Council

Executing Agency

Executive Engineer J&K Sports Council, Srinagar

Block/ District

Srinagar

AA Cost (Rs in lakhs)

12.00 lacs

Total Cost of completion / Expenditure ending 3/2022

7,18,944/=

Date of Start (Month / Year)

11/08/2021

Date of Completion (Month / Year)

March 2022

No` . of Beneficiaries.

1000


**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>7</b>
<b>Name of the work / project with location</b>	<b>Development of play field at TRC Srinagar by way of Seating Tier with adjustable seats for pavilion block.</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>15.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>8,65,050/=</b>
<b>Date of Start (Month / Year)</b>	<b>03/08/2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>500</b>

**Geo-Tagged Photograph  
1)**

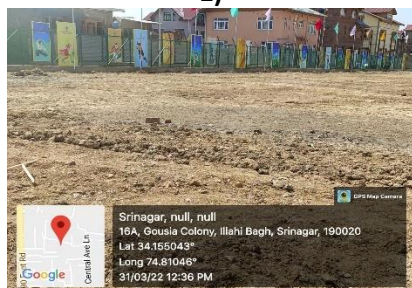


**With brief description of the project.**

<b>S.No.</b>	<b>8</b>
<b>Name of the work / project with location</b>	<b>External development and allied works for Indoor Sports hall at Illahi Bagh Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>128.05 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>70,04,387/=</b>
<b>Date of Start (Month / Year)</b>	<b>12/10/2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>1000</b>




**Geo-Tagged Photograph  
1)**

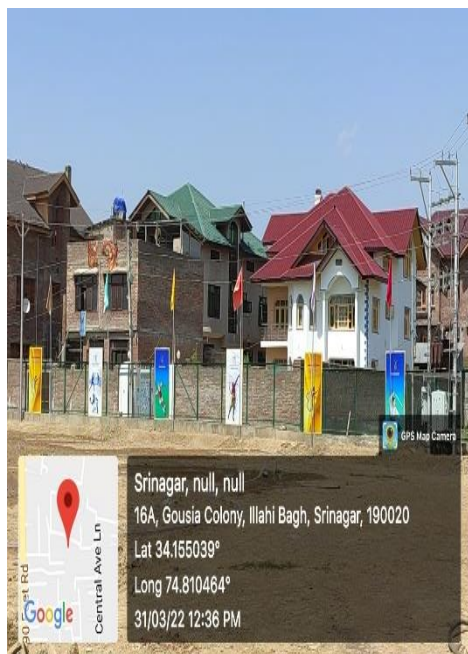

**With brief description of the project.**

<b>S.No.</b>	<b>9</b>
<b>Name of the work / project with location</b>	External development of Indoor Sports Hall at Zadibal (Site changed to illahibagh Srinagar by way of ACP Hoardings
<b>Department /organization</b>	YSS/ J&K Sports Council
<b>Executing Agency</b>	Executive Engineer J&K Sports Council, Srinagar
<b>Block/ District</b>	Srinagar
<b>AA Cost (Rs in lakhs)</b>	19.936 lacs
<b>Total Cost of completion / Expenditure ending 3/2022</b>	8,60,098/=
<b>Date of Start (Month / Year)</b>	30/11/2021
<b>Date of Completion (Month / Year)</b>	March 2022
<b>No` . of Beneficiaries.</b>	1000

**Geo-Tagged Photograph  
1)**

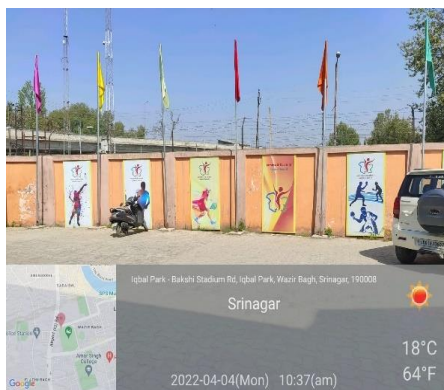

**With brief description of the project.**

<b>S.No.</b>	<b>10</b>
<b>Name of the work / project with location</b>	Upgradation of Administrative Block Sports Council at Bakshi Stadium Srinagar.
<b>Department /organization</b>	YSS/ J&K Sports Council
<b>Executing Agency</b>	Executive Engineer J&K Sports Council, Srinagar
<b>Block/ District</b>	Srinagar
<b>AA Cost (Rs in lakhs)</b>	25.00 lacs
<b>Total Cost of completion / Expenditure ending 3/2022</b>	Rs. 21.86 lacs/= (incl. const. of office rooms)
<b>Date of Start (Month / Year)</b>	12/08/2021
<b>Date of Completion (Month / Year)</b>	March 2022
<b>No` . of Beneficiaries.</b>	200

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>11</b>
<b>Name of the work / project with location</b>	<b>Development of play field at Tumlehal Pulwama by way of earth filling, Net Practice Pitch, Competition Pitch and Chain Link Fencing</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>80.21 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 48.34 lacs</b>
<b>Date of Start (Month / Year)</b>	<b>12/08/2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>500</b>

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>12</b>
<b>Name of the work / project with location</b>	<b>Construction of Guard Room with pantry and wash rooms at TRC New Entrances Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>10.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 6,49,142/-</b>
<b>Date of Start (Month / Year)</b>	<b>10/2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>08</b>

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>13</b>
<b>Name of the work / project with location</b>	<b>Development of parking area, upgradation of seating tiers by Granite Marble, Construction of lavatory block, tile path incl. entrance, lighting to parking area, store sheds and matts, construction of Volleyball and Basketball Courts at KNS Radapora Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>Rs.125.00 lacs (Advertised Rs. 53.19 lacs)</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs.32.97 lacs</b>
<b>Date of Start (Month / Year)</b>	<b>14.01.2022</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>1000</b>

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>14</b>
<b>Name of the work / project with location</b>	<b>Development of Gani Memorial field by way of Construction of Synthetic Volleyball Court at Rajouri Kadal Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>Rs.11.71 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs.8,72,608/-</b>
<b>Date of Start (Month / Year)</b>	<b>30.11.2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>100</b>

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

<b>S.No.</b>	<b>15</b>
<b>Name of the work / project with location</b>	<b>Development of Gani Memorial field by way of Construction of Synthetic Volleyball Court at Rajouri Kadal Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>Rs.11.71 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs.8,72,608/-</b>
<b>Date of Start (Month / Year)</b>	<b>30.11.2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>100</b>



**Geo-Tagged Photograph**



1)

With brief description of the project.

<b>S.No.</b>	<b>16</b>
<b>Name of the work / project with location</b>	<b>Construction of Roller Skating rink/Roll skating court at Gindun Stadium Rajbagh Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>30.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>18,26,705/=</b>
<b>Date of Start (Month / Year)</b>	<b>11/08/2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>200</b>

**Geo-Tagged Photograph**



1)

With brief description of the project.

<b>S.No.</b>	<b>17</b>
<b>Name of the work / project with location</b>	<b>Construction of Change room / wash room and development of play field by way of installation of water station, flex hoarding flags, dustbins etc. at Shaheed I milat Lal Bazar Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>Rs.29.50 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>17,99,524/=</b>
<b>Date of Start (Month / Year)</b>	<b>Aug, 2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>200</b>

### Geo-Tagged Photograph



1)

With brief description of the project.

S.No.	18
Name of the work / project with location	Development of play field at Lal Bazar (Shaheed I Milat) by way of levelling / Turfing of field (Part-A).
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	10.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs.5,52,500/-
Date of Start (Month / Year)	28.05.2021
Date of Completion (Month / Year)	March 2022
No` . of Beneficiaries.	1000

### Geo-Tagged Photograph


1)



With brief description of the project.

S.No.	19
Name of the work / project with location	Construction of multipurpose indoor sports hall at Bijbehara district Anantnag
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Anantnag
AA Cost (Rs in lakhs)	Rs.400.00
Total Cost of completion / Expenditure ending 3/2022	Rs.366.60 lakhs
Date of Start (Month / Year)	11-05-2018
Date of Completion (Month / Year)	December 2021
No` . of Beneficiaries.	500

**Geo-Tagged Photograph**

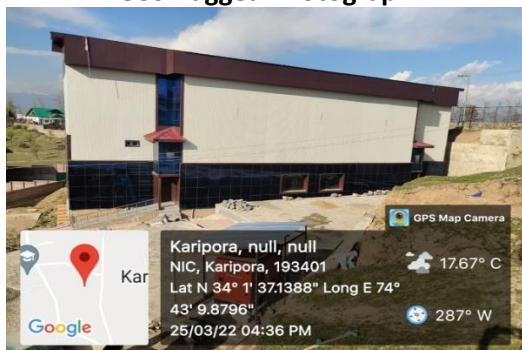

1)

**With brief description of the project.**

<b>S.No.</b>	<b>20</b>
<b>Name of the work / project with location</b>	<b>Construction of multipurpose indoor sports hall at Budgam (PEB incl. Civil sanitary &amp; Electrical Works)</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Budgam</b>
<b>AA Cost (Rs in lakhs)</b>	<b>400.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs.2,99,41,528/- (allotted cost)</b>
<b>Date of Start (Month / Year)</b>	<b>01/2020</b>
<b>Date of Completion (Month / Year)</b>	
<b>No` . of Beneficiaries.</b>	<b>500</b>

**Geo-Tagged Photograph**

1)



**With brief description of the project.**

<b>S.No.</b>	<b>21</b>
<b>Name of the work / project with location</b>	<b>Construction of multipurpose indoor sports hall at Illahibagh Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>Rs. 400.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 3,55,86,936/-</b>
<b>Date of Start (Month / Year)</b>	<b>26.11.2019</b>
<b>Date of Completion (Month / Year)</b>	<b>January 2022</b>
<b>No` . of Beneficiaries.</b>	<b>500</b>



With brief description of the project.

S.No.	22
Name of the work / project with location	Driver room and Canteen in Administrtive Block Bakhshi Stadium Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	20.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs.17.72 lacs (incl. wash Rooms and SDC Rooms)
Date of Start (Month / Year)	08/2021
Date of Completion (Month / Year)	March 2022
No`. of Beneficiaries.	200



With brief description of the project.

S.No.	23
Name of the work / project with location	Construction of Chowkidar Quarter at Pologround Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	10.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs.7.13 lacs
Date of Start (Month / Year)	08/2021
Date of Completion (Month / Year)	March 2022
No`. of Beneficiaries.	2




**Geo-Tagged Photograph  
1)**



**With brief description of the project.**


<b>S.No.</b>	<b>24</b>
<b>Name of the work / project with location</b>	<b>Construction of Chowkidar Quarter at Indoor Sports Hall Shadipora Bandipora</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Bandipora</b>
<b>AA Cost (Rs in lakhs)</b>	<b>12.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs.7.08 lacs</b>
<b>Date of Start (Month / Year)</b>	<b>Oct.,2021</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>2</b>


**Geo-Tagged Photograph  
1)**

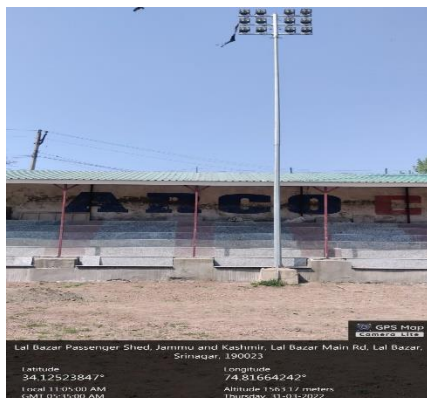

**With brief description of the project.**

<b>S.No.</b>	<b>25</b>
<b>Name of the work / project with location</b>	<b>Upgradation of seating tiers at Shaheed I Milat play field Lal bazaar Srinagar</b>
<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
<b>Block/ District</b>	<b>Srinagar</b>
<b>AA Cost (Rs in lakhs)</b>	<b>35.00 lacs</b>
<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 16.87 lacs</b>
<b>Date of Start (Month / Year)</b>	<b>02/2022</b>
<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
<b>No` . of Beneficiaries.</b>	<b>500</b>
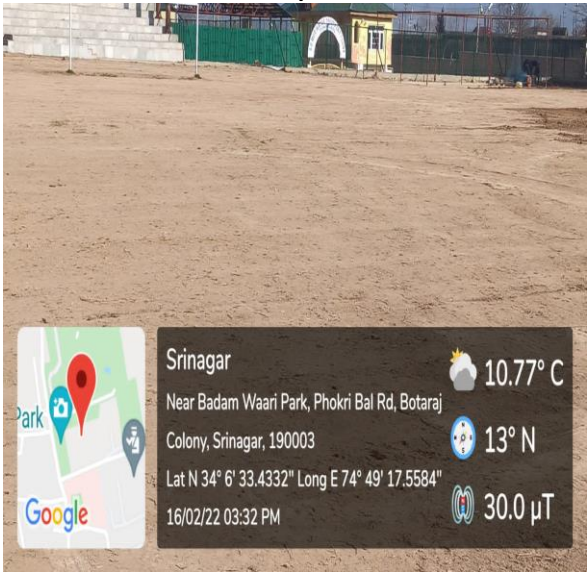
<p style="text-align: center;"><b>Geo-Tagged Photograph</b> 1)</p> 	<b>S.No.</b>	<b>26</b>
	<b>Name of the work / project with location</b>	<b>Dev. Of play ground at Bagh-i-Waris Khan Badamwari, Srinagar by way of renovation of existing pavilion building, earth filling &amp; turfing, restoration of damaged chain link. Fencing and construction of R/Wall with steps construction of 01 practice cricket pitch lighting</b>
	<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
	<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	<b>Block/ District</b>	<b>Srinagar</b>
	<b>AA Cost (Rs in lakhs)</b>	<b>46.70 lacs</b>
	<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 28.05 lacs</b>
	<b>Date of Start (Month / Year)</b>	<b>02/2022</b>
	<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
	<b>No` . of Beneficiaries.</b>	<b>500</b>
<b>With brief description of the project.</b>		

<p style="text-align: center;"><b>Geo-Tagged Photograph</b> 1)</p> 	<b>S.No.</b>	<b>27</b>
	<b>Name of the work / project with location</b>	<b>SITC of Flood Lighting System at Synthetic Hockey Field at Pologround Srinagar.</b>
	<b>Department /organization</b>	<b>YSS/ J&amp;K Sports Council</b>
	<b>Executing Agency</b>	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	<b>Block/ District</b>	<b>Srinagar</b>
	<b>AA Cost (Rs in lakhs)</b>	<b>150.00 lacs</b>
	<b>Total Cost of completion / Expenditure ending 3/2022</b>	<b>Rs. 150.00 lacs</b>
	<b>Date of Start (Month / Year)</b>	<b>Dec, 2021</b>
	<b>Date of Completion (Month / Year)</b>	<b>March 2022</b>
	<b>No` . of Beneficiaries.</b>	<b>300</b>
<b>With brief description of the project.</b>		

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**


S.No.	28
Name of the work / project with location	SITC of Flood Lighting System at Synthetic Rugby Field at Pologround Srinagar.
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	150.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 150.00 lacs
Date of Start (Month / Year)	12/2021
Date of Completion (Month / Year)	March 2022
No` . of Beneficiaries.	300

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	29
Name of the work / project with location	SITC of Flood Lighting System at Cricket Field at TRC Srinagar.
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	50.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 50.00 lacs
Date of Start (Month / Year)	Dec.,2021
Date of Completion (Month / Year)	March 2022
No` . of Beneficiaries.	500
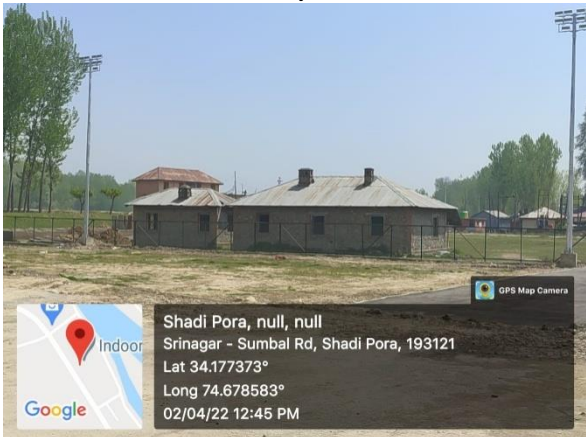
<p style="text-align: center;"><b>Geo-Tagged Photograph 1)</b></p>  <p style="text-align: center;"><b>With brief description of the project.</b></p>	S.No.	<b>30</b>
	Name of the work / project with location	<b>Illumination of Car parking and approach road at Indoor Sports Hall Shadipora Bandipora</b>
	Department /organization	<b>YSS/ J&amp;K Sports Council</b>
	Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	Block/ District	<b>Bandipora</b>
	AA Cost (Rs in lakhs)	<b>30.00 lacs</b>
	Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 30.00 lacs</b>
	Date of Start (Month / Year)	<b>12/2021</b>
	Date of Completion (Month / Year)	<b>March, 22</b>
	No` . of Beneficiaries.	<b>300</b>

<p style="text-align: center;"><b>Geo-Tagged Photograph 1)</b></p>  <p style="text-align: center;"><b>With brief description of the project.</b></p>	S.No.	<b>31</b>
	Name of the work / project with location	<b>Providing of flood lights at Sports Stadium Kulgam (Qoimoh)</b>
	Department /organization	<b>YSS/ J&amp;K Sports Council</b>
	Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	Block/ District	<b>Kulgam</b>
	AA Cost (Rs in lakhs)	<b>100.00 lacs</b>
	Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 100.00 lacs</b>
	Date of Start (Month / Year)	<b>12/2021</b>
	Date of Completion (Month / Year)	<b>March 2022</b>
	No` . of Beneficiaries.	<b>300</b>



**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	32
Name of the work / project with location	Development of play field by way of earth filling and turfing at Lasjan.
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	32.45 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 21.74 lacs
Date of Start (Month / Year)	Feb, 2022
Date of Completion (Month / Year)	Nov/2021
No` . of Beneficiaries.	1000

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	33
Name of the work / project with location	Upgradation of Pavilion Block at Pulwama Stadium
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Pulwama
AA Cost (Rs in lakhs)	25.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 15.94 lacs
Date of Start (Month / Year)	Feb, 2021
Date of Completion (Month / Year)	Oct/2021
No` . of Beneficiaries.	1000

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**


S.No.	34
Name of the work / project with location	Development of Cricket ground / football ground by way of construction of Volleyball and Basketball Court / earth filling etc. at Goripora Noorbagh Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	Rs. 16.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 8.66 lacs
Date of Start (Month / Year)	Feb, 2021
Date of Completion (Month / Year)	Dec,2021
No` . of Beneficiaries.	800


**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	35
Name of the work / project with location	Development of play field at Govt. High School Goripora Sopore
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Baramulla
AA Cost (Rs in lakhs)	Rs. 6.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 3.78 lacs
Date of Start (Month / Year)	Sept, 2021
Date of Completion (Month / Year)	Dec/2021
No` . of Beneficiaries.	1000

<p><b>Geo-Tagged Photograph 1)</b></p> 	S.No.	<b>36</b>
	Name of the work / project with location	<b>Development of play field at Govt. High School Tujjar Sopore</b>
	Department /organization	<b>YSS/ J&amp;K Sports Council</b>
	Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	Block/ District	<b>Baramulla</b>
	AA Cost (Rs in lakhs)	<b>Rs. 6.00 lacs</b>
	Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 4.02 lacs</b>
	Date of Start (Month / Year)	<b>Sept, 2021</b>
	Date of Completion (Month / Year)	<b>Dec/2021</b>
	No` . of Beneficiaries.	<b>1000</b>
<p><b>With brief description of the project.</b></p>		

<p><b>Geo-Tagged Photograph 1)</b></p> 	S.No.	<b>37</b>
	Name of the work / project with location	<b>Development of play field at Heing Tangmarg by way of earthwork in cutting / filling and chain link fencing.</b>
	Department /organization	<b>YSS/ J&amp;K Sports Council</b>
	Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
	Block/ District	<b>Baramulla</b>
	AA Cost (Rs in lakhs)	<b>Rs. 34.84 lacs</b>
	Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 24.03 lacs</b>
	Date of Start (Month / Year)	<b>Sept, 2020</b>
	Date of Completion (Month / Year)	<b>Sept/2021</b>
	No` . of Beneficiaries.	<b>1200</b>
<p><b>With brief description of the project.</b></p>		



**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	<b>38</b>
Name of the work / project with location	<b>Providing chain link fencing and entrance gate to play ground at Kutlari Mawar Langate</b>
Department /organization	<b>YSS/ J&amp;K Sports Council</b>
Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
Block/ District	<b>Kupwara</b>
AA Cost (Rs in lakhs)	<b>Rs. 14.92 lacs</b>
Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 11.19 lacs</b>
Date of Start (Month / Year)	<b>Sept,2021</b>
Date of Completion (Month / Year)	<b>March/2022</b>
No` . of Beneficiaries.	<b>1200</b>

**Geo-Tagged Photograph  
1)**



**With brief description of the project.**

S.No.	<b>39</b>
Name of the work / project with location	<b>Repairs to Showkat Ali Stadium Pavilion block incl. Providing and fixing Ceiling (District Baramulla)</b>
Department /organization	<b>YSS/ J&amp;K Sports Council</b>
Executing Agency	<b>Executive Engineer J&amp;K Sports Council, Srinagar</b>
Block/ District	<b>Baramulla</b>
AA Cost (Rs in lakhs)	<b>Rs. 13.00 lacs</b>
Total Cost of completion / Expenditure ending 3/2022	<b>Rs. 8.32 lacs</b>
Date of Start (Month / Year)	<b>Sept, 2021</b>
Date of Completion (Month / Year)	<b>March,2022</b>
No` . of Beneficiaries.	<b>800</b>



**Geo-Tagged Photograph  
1)**



**With brief description of the project.**


S.No.	40
Name of the work / project with location	Development of Mini play field at Wangath Kangan by way of earth cutting, construction of protection wall and Toe Wall and Providing ChainLink fencing.
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Ganderbal
AA Cost (Rs in lakhs)	Rs. 20.27 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 13.37 lacs
Date of Start (Month / Year)	Feb, 2021
Date of Completion (Month / Year)	Feb/2022
No` . of Beneficiaries.	250


**Geo-Tagged Photograph  
1)**




**With brief description f the project.**

S.No.	41
Name of the work / project with location	Development of play field at Amda Kadal Srinagar by way of earth in cutting / filling, construction of drain, painting and electrification.
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	Rs. 16.00 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 11.64 lacs
Date of Start (Month / Year)	Feb, 2021
Date of Completion (Month / Year)	Oct/2021
No` . of Beneficiaries.	400

<p><b>Geo-Tagged Photograph 1)</b></p> 	S.No.	42
	Name of the work / project with location	Providing and fixing of grill fencing at office block for parking at Pologround Srinagar
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Srinagar
	AA Cost (Rs in lakhs)	Rs. 7.50 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs. 4.38 lacs
	Date of Start (Month / Year)	03/2021
	Date of Completion (Month / Year)	08/2021
	No` . of Beneficiaries.	200
With brief description of the project.		

<p><b>Geo-Tagged Photograph 1)</b></p> 	S.No.	43
	Name of the work / project with location	SITC of Gen Set 82.5 KVA and other allied required / related accessories incl. civil works and annual maintenance for a period of three years at Anjum play field Bemina Srinagar
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Srinagar
	AA Cost (Rs in lakhs)	Rs. 8.80 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs. 8.80 lacs
	Date of Start (Month / Year)	08/2021
	Date of Completion (Month / Year)	11/2021
	No` . of Beneficiaries.	400
With brief description of the project.		


**Geo-Tagged Photograph  
1)**

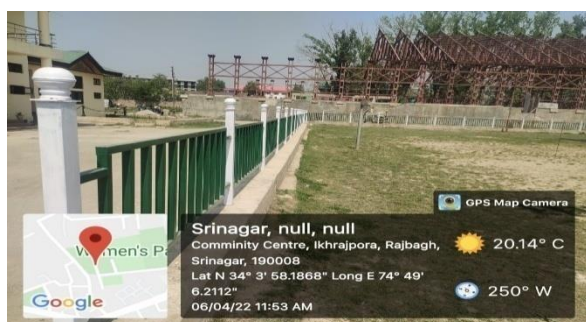

**With brief description of the project.**


S.No.	44
Name of the work / project with location	Development of Gindun Park by way of grill fencing, curb stone, car parking, earth filling, restoration of cafeteria building and landscaping
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	Rs. 54.41 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 31.06 lacs
Date of Start (Month / Year)	05/2021
Date of Completion (Month / Year)	March/2022
No` . of Beneficiaries.	500


**Geo-Tagged Photograph  
1)**

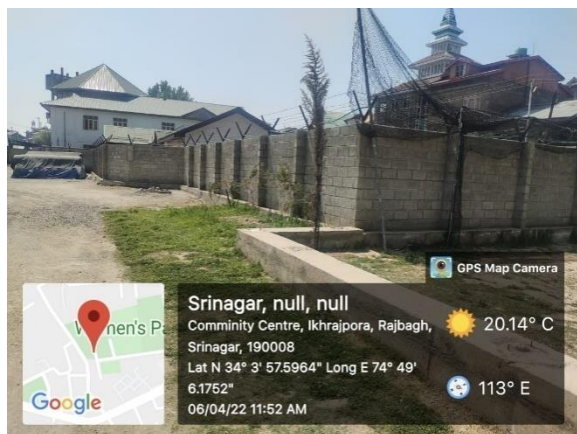

**With brief description of the project.**

S.No.	45
Name of the work / project with location	Construction of Compound walling at SKMSAC, Gindun Rajbagh Srinagar
Department /organization	YSS/ J&K Sports Council
Executing Agency	Executive Engineer J&K Sports Council, Srinagar
Block/ District	Srinagar
AA Cost (Rs in lakhs)	Rs. 10.10 lacs
Total Cost of completion / Expenditure ending 3/2022	Rs. 6.91 lacs
Date of Start (Month / Year)	07/2020
Date of Completion (Month / Year)	March/2021
No` . of Beneficiaries.	300

<p><b>Geo-Tagged Photograph</b> 1)</p>  <p>Latitude: 34.027381 Longitude: 74.719122 Elevation: 1655.79m Accuracy: 27.1m Time: 03-24-2022 17:36 Note: Budgam</p>	S.No.	46
	Name of the work / project with location	External development and allied works for Indoor Sports Hall at Budgam
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Budgam
	AA Cost (Rs in lakhs)	Rs. 74.12 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs. 41.73 lacs
	Date of Start (Month / Year)	Oct., 2021
	Date of Completion (Month / Year)	March/2022
With brief description of the project.	No` . of Beneficiaries.	1000

<p><b>Geo-Tagged Photograph</b> 1)</p>  <p>Baramulla, null, null Baramulla, Baramulla Rd, Srinagar Area, Baramulla, 193103 India, 34.027381, 74.719122 06/04/22 12:51 PM</p>	S.No.	47
	Name of the work / project with location	TT tables, furniture, canopies, for inauguration of indoor sports stadium at Baramulla.
	Department /organization	YSS/ J&K Sports Council
	Executing Agency	Executive Engineer J&K Sports Council, Srinagar
	Block/ District	Baramulla
	AA Cost (Rs in lakhs)	Rs. 10.00 lacs
	Total Cost of completion / Expenditure ending 3/2022	Rs. 8.99 lacs
	Date of Start (Month / Year)	01/2020
	Date of Completion (Month / Year)	01/2020
With brief description of the project.	No` . of Beneficiaries.	1000





Sr No.	48
Name of the work with location	Construction of Driver room at MA Stadium Lat : 32.7240 Long:74.8560
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex. En.J&K Sports Council, Jammu
Block / District	Jammu
AA Cost (in lacs )	20.00
Expenditure incurred ending 3/2022	8.00
DOS	Oct 2021
DOC	March 2022



Sr No.	49
Name of the work with location	Construction of Lawn tennis Court 2 No. Lat : 32.7227 Long:74.8556
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex.En.J&K Sports Council, Jammu
Block / District	Jammu
AA Cost (in lacs )	100.00
Expenditure incurred ending 3/2022	20.75
DOS	Dec 2021
DOC	March 2022
No. of Beneficiaries	500



Sr No.	50
Name of the work with location	Additional facilities like drinking water, flags, lights, Sinage board etc in Indoor Sports Hall at Billawar Kathua. Lat : 32.615924 Long:75.601534
Department /Organization	J&K Sports Council
Executive Agency	Ex. En. J&K Sports Council, Jammu
Block / District	Kathua billawar
AA Cost (in lacs )	26.20
Expenditure incurred ending 3/2022	8.46
DOS	Dec 2021
DOC	Feb 2022
No. of Beneficiaries	1000




Sr No.	51
Name of the work with location	Additional facilities like drinking water, flags, Sinage board etc in Sports Stadium Kathua Lat : 32.375179 Long:75.515579
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex. En J&K Sports Council, Jammu
Block / District	Kathua
AA Cost (in lacs )	3.70
Expenditure incurred ending 3/2022	2.20
DOS	Nov 2021
DOC	Feb 2022
No. of Beneficiaries	1000



Sr No.	52
Name of the work with location	Const. of Chowkidar Quarter at Indoor Stadium Billawar Lat : 32.375179 Long:75.515579
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex. En.J&K Sports Council, Jammu
Block / District	Kathua billawar
AA Cost (in lacs )	15.00
Expenditure incurred ending 3/2022	10.44
DOS	March 2021
DOC	Feb 2022
No. of Beneficiaries	02



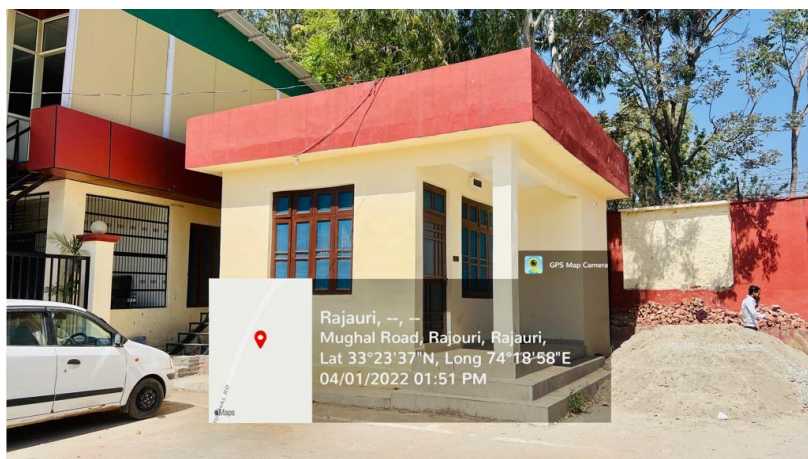

Sr No.	53
Name of the work with location	Construction of Chowkidar Quarter Sports Stadium at Rajouri Lat: Long :
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex. En.J&K Sports Council,Jammu
Block / District	Rajauri
AA Cost (in lacs )	20.00
Expenditure incurred ending 3/2022	10.31
DOS	March 2021
DOC	March 2022
No. of Beneficiaries	02



Sr No.	54
Name of the work with location	Additional facilities like upgradation of existing Sitting tiers , drinking water, flags, Sinage board etc at play field at Shastri Nagar Lat: 32.6956 Long: 74.8571
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex En J&K Sports Council ,Jammu
Block / District	Jammu
AA Cost (in lacs )	16.94
Expenditure incurred ending 3/2022	10.55
DOS	Sept 2021
DOC	March 2022
No. of Beneficiaries	1000





Sr No.	55
Name of the work with location	Levelling of additional ground near playfield at Salmeri Samba Lat:33.5768 Long:75.0070
Department/Organization	Yss/J&K Sports Council
Executive Agency	Ex En J&K Sports Council ,Jammu
Block / District	Samba
AA Cost (in lacs )	22.00
Expenditure incurred ending 3/2022	3.53
DOS	Sept 2021
DOC	March 2022
No. of Beneficiaries	1000



Sr No.	56
Name of the work with location	P/F of 5 No. Collapsible gates at Indoor hall Ram Nagar Lat: 32.81 Long:75.3161
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex En J&K Sports Council ,Jammu
Block / District	Udhampur
AA Cost (in lacs )	7.00
Expenditure incurred ending 3/2022	2.21
DOS	Oct 2021
DOC	March 2022
No. of Beneficiaries	200



Sr No.	57
Name of the work with location	Additional facilities like raising of Chainlink fencing, Sitting tiers, drinking water, flags, Sinage board, ground water facilities etc at play field at Green filed Gandhi Nagar Lat: 32.7109 Long: 74.8617
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council ,Jammu
Block / District	Jammu
AA Cost (in lacs )	50.00
Expenditure incurred ending 3/2022	31.17
DOS	Oct 2021
DOC	March 2022
No. of Beneficiaries	1000



Sr No.	58
Name of the work with location	Additional facilities like drinking water, Sitting tiers flags, Change room , Sinage board etc at Playfiled GGM Science collage Jammu Lat: Long:
Department/Organiz ation	YSSJ&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	49.13
Expenditure incurred ending 3/2022	20.21
DOS	Nov. 2021
DOC	March 2022
No. of Beneficiaries	1500





Sr No.	59
<b>Name of the work with location</b>	<b>Additional facilities like drinking water, flags, Sinage board etc in Indoor Sports Hall at Ramnagar Udhampur. Lat: Long:</b>
<b>Department/Organization</b>	<b>YSS/J&amp;K Sports Council</b>
<b>Executive Agency</b>	<b>Ex EnJ&amp;K Sports Council Jammu</b>
<b>Block / District</b>	<b>Jammu</b>
<b>AA Cost (in lacs )</b>	<b>8.90</b>
<b>Expenditure incurred ending 3/2022</b>	<b>8.90</b>
<b>DOS</b>	<b>Nov. 2021</b>
<b>DOC</b>	<b>March 2022</b>
<b>No. of Beneficiaries</b>	<b>1500</b>



Sr No.	60
<b>Name of the work with location</b>	<b>Additional facilities like drinking water, flags, lights, Sinage board etc in Indoor Sports Hall at Rajouri Kotranka. Lat:-33.3615 Long:-74.5140</b>
<b>Department /Organization</b>	<b>YSS/J&amp;K Sports Council</b>
<b>Executive Agency</b>	<b>Ex EnJ&amp;K Sports Council Jammu</b>
<b>Block / District</b>	<b>Jammu</b>
<b>AA Cost (in lacs )</b>	<b>8.90</b>
<b>Expenditure incurred ending 3/2022</b>	<b>4.65</b>
<b>DOS</b>	<b>Oct. 2021</b>
<b>DOC</b>	<b>March 2022</b>
<b>No. of Beneficiaries</b>	<b>1000</b>



Sr No.	61
Name of the work with location	Additional facilities like drinking water, flags, Sinage board,etc at New Indoor Sports M.A.Stadium. Lat:-33.3615 Long:-74.5140
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	2.85
Expenditure incurred ending 3/2022	2.08
DOS	Dec. 2021
DOC	March 2022
No. of Beneficiaries	1000



Sr No.	62
Name of the work with location	Construction of parking zone by way of P/L Cement railing, interlocking of tiles at M.A. Stadium Jammu Lat:-32.7239 Long:-74.8555
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	111.20
Expenditure incurred ending 3/2022	75.00
DOS	Dec. 2020
DOC	March 2022
No. of Beneficiaries	1000





Sr No.	63
Name of the work with location	Additional facilities like drinking water, flags, Sinage board etc in Play field Purmandal Lat:-32.68929 Long:-75.055333
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex En J&K Sports Council jammu
Block / District	Jammu
AA Cost (in lacs )	8.90
Expenditure incurred ending 3/2022	7.48
DOS	Dec 2021
DOC	March 2022
No. of Beneficiaries	500



Sr No.	64
Name of the work with location	Construction of Cricket pitches and procurement of mats/poles at Mendhar College Lat:-32.68929 Long:-75.055333
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	MendharPoonch
AA Cost (in lacs )	12.00
Expenditure incurred ending 3/2022	4.47
DOS	May 2021
DOC	Feb 2022
No. of Beneficiaries	500



Sr No.	65
Name of the work with location	Construction of playground at High School at Mehari Gujran Rajouri by way of levelling of ground, Gender based Toilet, Gate with Pillars, Chain link fencing and sitting tiers Lat:-33.347262 Longi:-74.2771179
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Mehari gujran Rajouri
AA Cost (in lacs )	51.10
Expenditure incurred ending 3/2022	17.84
DOS	April 2021
DOC	march 2022




Sr No.	66
Name of the work with location	Additional facilities like drinking water, flags, Sinage board etc in Play field Salmeri Vijaypur Lat:-32.576811 Longi:-75.00482
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Salmeri vijaypur samba
AA Cost (in lacs )	8.90
Expenditure incurred ending 3/2022	2.36
DOS	september 2021
DOC	feb 2022
No. of Beneficiaries	500





Sr No.	67
Name of the work with location	Construction of Chowkidar quarter at Indoor Stadium Samba Lat:-32.571191 Long:-75.112642
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	samba
AA Cost (in lacs )	10.00
Expenditure incurred ending 3/2022	8.50
DOS	JAN 2021
DOC	JULY 2021
No. of Beneficiaries	500

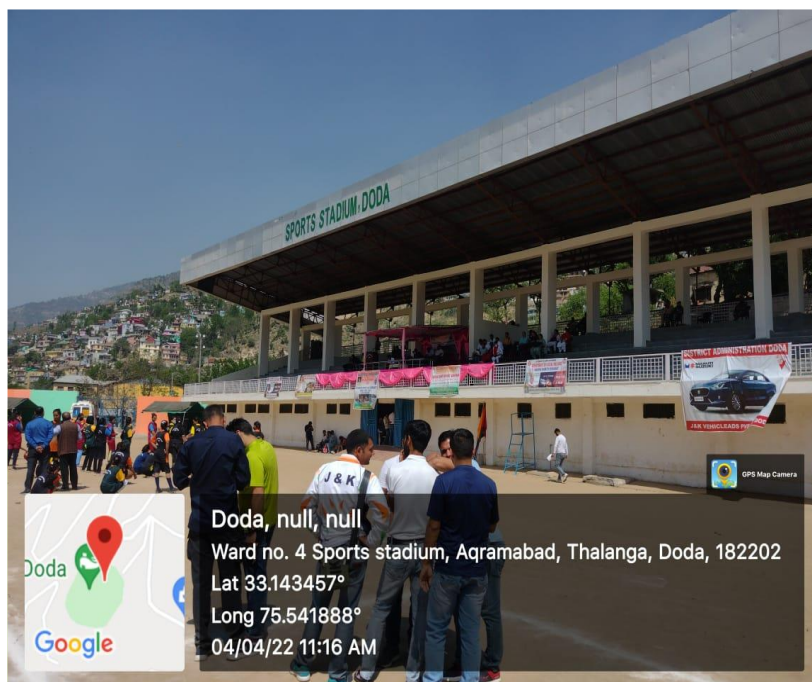

Sr No.	68
Name of the work with location	Upgradation of Sports Stadium D Doda by way of various works Lat:-33.143457 Long:-75.541
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Doda
AA Cost (in lacs )	10.00
Expenditure incurred ending 3/2022	5.00
DOS	Nov 2021
DOC	Feb 2022
No. of Beneficiaries	1500



Sr No.	69
Name of the work with location	Additional facilities like drinking water, flags, High Mast Lights, Compound Wall, Sinage board, Pucca drain etc Sports stadium Doda Lat:-33.1428 Long:-75.5418
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Doda
AA Cost (in lacs )	25.00
Expenditure incurred ending 3/2022	12.50
DOS	Dec 2021
DOC	March 2022
No. of Beneficiaries	1500



Sr No.	70
Name of the work with location	Const. of compound walling/sitting tiers and filling of good earth on Govt. Middle School Chak Battal, Hiranagar
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Hira Nagar Kathua
AA Cost (in lacs )	5.00
Expenditure incurred ending 3/2022	2.50
DOS	April 2015
DOC	March 2022
No. of Beneficiaries	300






Sr No.	71
Name of the work with location	Additional facilities like drinking water, flags, Sinage board etc M.A Stadium Lat;32.723033 Lon;74.8522
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	8.90
Expenditure incurred ending 3/2022	1.76
DOS	Dec 2021
DOC	FEB 2022
No. of Beneficiaries	1500



Sr No.	72
Name of the work with location	Face lifting of old Indoor Sports Complex on road side MA Stadium/ Mini Stadium Jammu. Lat;32.7220 Lon;74.8553
Department/Organiz ation	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	3.00
Expenditure incurred ending 3/2022	3.00
DOS	Dec 2020
DOC	March 2022
No. of Beneficiaries	200



Sr No.	73
Name of the work with location	Up-Garadation/ Chain link fencing around Sports House at M.A.Stadium Jammu Lat;32.7283 Lon;74.8563
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	20.00
Expenditure incurred ending 3/2022	10.00
DOS	Sept 2021
DOC	Oct 2021
No. of Beneficiaries	200

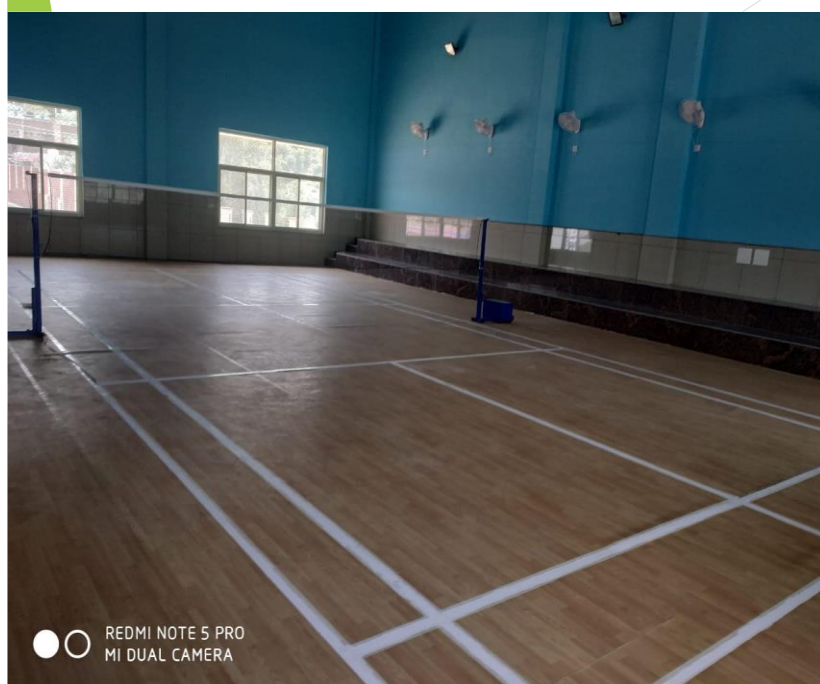

Sr No.	74
Name of the work with location	Laying of Sports Flooring for various activities in Indoor Hall Rajouri Lat; 33.392985 Lon;74.316893
DepartmentOrganization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	30.00
Expenditure incurred ending 3/2022	30.00
DOS	Sept 2021
DOC	Nov 2021
No. of Beneficiaries	1000





Sr No.	75
Name of the work with location	Up-Garadation of Various locations of MA Stadium by way of improvement of paths . Lat;32.7240 Lon;74.8533
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	55.00
Expenditure incurred ending 3/2022	55.00
DOS	July 2021
DOC	Nov 2021
No. of Beneficiaries	1000



Sr No.	76
Name of the work with location	Development of Volleyball Court at Kothra Darhal by way of Chainlink fencing Lat : Lon:
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex. En.J&K Sports Council , Jammu
Block / District	Darhal Rajouri
AA Cost (in lacs )	34.95
Expenditure incurred ending 3/2022	14.37
DOS	Feb 2020
DOC	March 2021
No. of Beneficiaries	1000








Sr No.	77
Name of the work with location	Providing and fixing of Sports Chairs and led light including wiring at Indoor Sports Hall Billawar Kathua Lat : 32.615924 Long:75.601534
Department/Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Billawar Kathua
AA Cost (in lacs )	13.70
Expenditure incurred ending 3/2022	13.70
DOS	May 2018
DOC	March 2022
No. of Beneficiaries	1000





Sr No.	78
Name of the work with location	P/F of chainlink fencing around Green field Gandhi Nagar Lat :32.710691 lon:74.861545
Department /Organization	YSS/J&K Sports Council
Executive Agency	Ex EnJ&K Sports Council Jammu
Block / District	Jammu
AA Cost (in lacs )	28.00
Expenditure incurred ending 3/2022	14.00
DOS	Jan 2022
DOC	March 2022
No. of Beneficiaries	1000


 <p>MS Anungala</p> <p>Bathole, null, null DIST REASI, Bathole, 182315 Lat 33.333055° Long 74.894272° 19/02/22 02:36 PM</p>	S.No	79
	Name of the work with location	Development of playfield at Govt. MS Anungala
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Reasi
	AA Cost (Rs. in Lakhs)	5.00
	Total Cost of completion/Expenditure incurred ending 03/2022	4.75
	Date of Start (Month/Year)	2018-19
	Date of completion(Month/Year)	Mar-22
	No. of beneficiaries	50

 <p>HS Chinkah</p> <p>Matlot Wednesday, 29/12/2021 Unnamed Road, Matlot, 185201 Lat N 33° 11' 0.0096" Long E 74° 48' 6.426"</p>	S.No	80
	Name of the work with location	Development of playfield at Govt HS Chinkah *
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Reasi
	AA Cost (Rs. in Lakhs)	5.61
	Total Cost of completion/Expenditure incurred ending 03/2022	5.37
	Date of Start (Month/Year)	2017-18
	Date of completion(Month/Year)	Mar-22
	No. of beneficiaries	100


 <p>PSMuttas</p> <p>Baddar, null, null Budhal-Ramban Rd, Baddar Lat 33.318046° Long 74.66439° 05/04/22 02:13 PM</p>	S.No	81
	Name of the work with location	Development of playfield at GovtPS Muttas
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Reasi
	AA Cost (Rs. in Lakhs)	4.00
	Total Cost of completion/Expenditure incurred ending 03/2022	3.95
	Date of Start (Month/Year)	2021-22
	Date of completion(Month/Year)	Mar-22
	No. of beneficiaries	16


	S.No	82
	Name of the work with location	Construction of Cricket Wicket Net at MS GulabGarhPaddar
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	Ex En JKSC J/K
	Block/District	Paddar / Kishtwar
	AA Cost (Rs. in Lakhs)	4.85
	Total Cost of completion/Expenditure incurred ending 03/2022	2.33
	Date of Start (Month/Year)	Nov. 2021
	Date of completion(Month/Year)	Feb. 2022
	No. of beneficiaries	300


	S.No	83
	Name of the work with location	Improvement of Sports Stadium GulabGarhPaddar
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Paddar / Kishtwar
	AA Cost (Rs. in Lakhs)	10.00
	Total Cost of completion/Expenditure incurred ending 03/2022	6.67
	Date of Start (Month/Year)	Aug 2021
	Date of completion(Month/Year)	Feb 2022
	No. of beneficiaries	300


	S.No	84
	Name of the work with location	Const. of Concrete Badminton Court at HSS Palmar
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Palmar / Kishtwar
	AA Cost (Rs. in Lakhs)	4.22
	Total Cost of completion/Expenditure incurred ending 03/2022	3.19
	Date of Start (Month/Year)	Aug 2021
	Date of completion(Month/Year)	Mar 2022
	No. of beneficiaries	150





	S.No	85
	Name of the work with location	Const. of Concrete Badminton Court at HS Pochhal
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Kishtwar
	AA Cost (Rs. in Lakhs)	3.77
	Total Cost of completion/Expenditure incurred ending 03/2022	2.95
	Date of Start (Month/Year)	Aug 2021
	Date of completion(Month/Year)	Mar 2022
	No. of beneficiaries	200

	S.No	86
	Name of the work with location	Const. of Concrete Badminton Court at MS City Boys Kishtwar
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	PWD
	Block/District	Kishtwar
	AA Cost (Rs. in Lakhs)	4.22
	Total Cost of completion/Expenditure incurred ending 03/2022	1.39
	Date of Start (Month/Year)	Oct 2021
	Date of completion(Month/Year)	Mar 2022
	No. of beneficiaries	250

	Sr.No.	87
	Name of work with location	Development of playfield at HSS Dhanas Zone Chenani, by way of Construction of Concrete Badminton court
	Department/ Organization	YSS/Directorate of YSS
	Executing Agency	RDD
	Block/District	Chenani/ Udampur
	AA cost (Rs. In lakhs)	4.00
	Total cost of completion /Expenditure incurred ending 03/2022	1.68
	Date of Start (Month/Year)	11/2021
	Date of Completion (Month/Year)	03/2022
	No. of Beneficiaries	250

 <p>Latitude 32.879620° Longitude 75.171361° LOCAL 11:59:25 MONDAY 04.04.2022 GMT 06:29:25 ALTITUDE 2109 FEET</p>	Sr.No.	<b>88</b>
	Name of work with location	Establishment of Sports Infrastructure/ Pavilion at HSS Jaganoo, by way of Filling of Good earth, leveling, Installation of Volleyball, Kho-Kho, Handball Poles
	Department/ Organization	YSS/Directorate of YSS
	Executing Agency	RDD
	Block/District	Jaganoo/ Udhampur
	AA cost (Rs. In lakhs)	4.00
	Total cost of completion /Expenditure incurred ending 03/2022	2.05
	Date of Start (Month/Year)	11/2021
	Date of Completion (Month/Year)	03/2022
	No. of Beneficiaries	200


 <p>Latitude 32.83689333333333° Longitude 75.26698166666667° Local 12:34:06 PM Altitude 813 meters GMT 07:04:06 AM Thursday, 31-03-2022</p>	Sr.No.	<b>89</b>
	Name of work with location	Development of playfield at HS NagrotaPanjgrain, Zone Ghordi Block Chanunta, construction of sitting steps etc.
	Department/ Organization	YSS/Directorate of YSS
	Executing Agency	RDD
	Block/District	Chanunta/ Udhampur
	AA cost (Rs. In lakhs)	3.00
	Total cost of completion /Expenditure incurred ending 03/2022	2.490
	Date of Start (Month/Year)	12/2021
	Date of Completion (Month/Year)	03/2022
	No. of Beneficiaries	200


 <p>Latitude 32.924454999999995° Longitude 75.13580666666667° Local 02:48:48 PM Altitude 738.7 meters GMT 09:18:48 AM Monday, 04-04-2022</p>	Sr.No.	<b>90</b>
	Name of work with location	Chain Link Fencing Handball Synthetic Court at Mini Stadium Udhampur
	Department/ Organization	YSS/Directorate of YSS
	Executing Agency	RDD
	Block/District	Udhampur/ Udhampur
	AA cost (Rs. In lakhs)	4.89
	Total cost of completion /Expenditure incurred ending 03/2022	4.770
	Date of Start (Month/Year)	12/2021
	Date of Completion (Month/Year)	03/2022
	No. of Beneficiaries	250


 <p>Latitude: 33.101159 Longitude: 75.59796 Elevation: 1662.2±100 m Accuracy: 3.6 m Time: 22-03-2022 16:31 Construction of Fencing/ Boundary Wall at MS Sindra</p>	Sr. No	91
	Name of the Work with location	Construction of Fencing/ Boundary Wall at MS Sindra
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Bhalla/Doda
	AA Cost (Rs. in lakhs)	2.88
	Total Cost of Completion/Expenditure incurred ending 03/2022	2.47
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	2900


 <p>Latitude: 33.055974 Longitude: 75.940714 Elevation: 1862.6±8 m Accuracy: 2.8 m Time: 22-03-2022 15:54 Note: construction of p/ work at HS Tilogra Zone Bhayyala Under P and DYSS Doda</p>	Sr. No	92
	Name of the Work with location	Construction of P/Work Play Ground HS Tilogra
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Jakyas/Doda
	AA Cost (Rs. in lakhs)	4.47
	Total Cost of Completion/Expenditure incurred ending 03/2022	1.54
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	2000

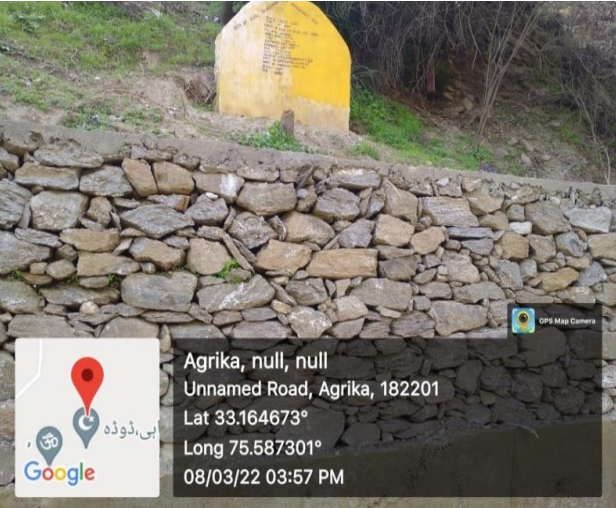


	Sr. No	93
	Name of the Work with location	Construction of Play Ground at UPS Shaie by way of Filling /Leveling /B. Wall Block Ghat.
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Ghat/ Doda
	AA Cost (Rs. in lakhs)	1.98
	Total Cost of Completion/Expenditure incurred ending 03/2022	0.99
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Dec-21
	No. of Beneficiaries	2500


	Sr. No	94
	Name of the Work with location	Construction of Play Ground at HS Kancha by way of Leveling /B. Wall
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Kahara/Doda
	AA Cost (Rs. in lakhs)	5.00
	Total Cost of Completion/Expenditure incurred ending 03/2022	3.79
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	3900

 <p>Latitude: 33.054054 Longitude: 75.943986 Elevation: 1687.54±16 m Accuracy: 10.0 m Time: 03-15-2022 11:54 Note: Constt. Of play ground UPS GUJJAR GOWARI PYT. TILOGRA U/HEAD</p>	Sr. No	95
	Name of the Work with location	Construction of P/Work Play Ground at UPS Gujjar GowariPyt. Tilogra Zone Bhatyas
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Jakyas/Doda
	AA Cost (Rs. in lakhs)	1.92
	Total Cost of Completion/Expenditure incurred ending 03/2022	0.74
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	2700

 <p>Latitude: 33.15032 Longitude: 75.486357 Accuracy: 3500.0 m Azimuth: 282° (W) Pitch: -24.0° (2.9°) Time: 22-03-2022 18:14 Note: consent of playground HSS Sazan by way leveling paint at Baser upper</p>	Sr. No	96
	Name of the Work with location	Construction of Play Ground at HSS Sazan by way of Leveling
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Bhagwah/Doda
	AA Cost (Rs. in lakhs)	2.50
	Total Cost of Completion/Expenditure incurred ending 03/2022	2.47
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	4000



 <p>Latitude: 33.08524 Longitude: 75.725037 Elevation: 1667.1m Accuracy: 9.6m</p>	Sr. No	97
	Name of the Work with location	Development of Play Field HS Gosti
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Chiralla/Doda
	AA Cost (Rs. in lakhs)	10.00
	Total Cost of Completion/Expenditure incurred ending 03/2022	4.94
	Date of Start (Month/Year)	2021
	Date of Completion (Month /Year)	Mar-22
	No. of Beneficiaries	3500

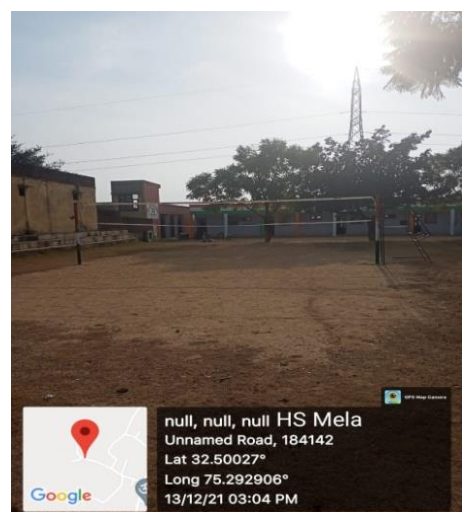

S.No	98
Name of the work with location	Dev. Of Playfield HS Mella, Hiranagar *
Department/organisation	YSS/Directorate of YSS
Executive Agency	ACD Kathua
Block/District	Hirangar/Kathua
AA Cost	3.00
Total Cost of Completion/Expenditure incurred ending 3/2022	2.73
Date of start (month/year)	2017-18
Date of Completion (month/year)	Mar-22
No. of Beneficiaries	700







S.No	99
Name of the work with location	Dev. Of playfield at HSS Kootah *
Department/organisation	YSS/Directorate of YSS
Executive Agency	ACD Kathua
Block/District	Hirangar/Kathua
AA Cost	3.00
Total Cost of Completion/Expenditure incurred ending 3/2022	2.75
Date of start (month/year)	2017-18
Date of Completion (month/year)	Mar-22
No. of Beneficiaries	800



S.No	100
Name of the work with location	Constt. Of Badminton Court at HSS Kathua (Boys) *
Department/organisation	YSS/Directorate of YSS
Executive Agency	Xen PWD Kathua
Block/District	Kathua
AA Cost	1.77
Total Cost of Completion/Expenditure incurred ending 3/2022	1.51
Date of start (month/year)	2018-19
Date of Completion (month/year)	Mar-22
No. of Beneficiaries	1000

 <p>HS JOURIAN</p>	S.No	101
	Name of the work with Location	Const. of Syn. Volley Ball Court at HS Jourian**
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	Ex En JK Sports Council J/K
	Block District	Jourian/ Jammu
	AA Cost (Rs. In Lakh)	15.50
	Total cost of completion/Exp. Incurred ending 3/2022	10.93
	Date of Start (Month/Year)	Feb-22
	Date of Completion (Month/Year)	30-03-2022
	No. of beneficiaries	2000

 <p>NARRI BALLA</p> <p>Tacharwan, null, null XQ84+F48, Tacharwan, 181201 Lat 32.965716° Long 74.755806° 25/03/22 04:08 PM</p>	S.No	102
	Name of the work with Location	Const. of Syn. Volley Ball Court at HSS Nariballa, Akhnoor
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	Ex En JK Sports Council J/K
	Block District	Akhnoor/ Jammu
	AA Cost (Rs. In Lakh)	15.5
	Total cost of completion/Exp. Incurred ending 3/2022	10.49(LAC)
	Date of Start (Month/Year)	Feb-22
	Date of Completion (Month/Year)	25-03-2022
	No. of beneficiaries	2000



S.No	103
Name of the work with Location	Const. of Syn. Volley Ball Court at MS Domana
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Akhnoor/ Jammu
AA Cost (Rs. In Lakh)	15.5
Total cost of completion/Exp. Incurred ending 3/2022	8.59(LAC)
Date of Start (Month/Year)	Feb-22
Date of Completion (Month/Year)	25-03-2022
No. of beneficiaries	2500




S.No	104
Name of the work with Location	Const. & Fencing of football Gound at Lower -C
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Akhnoor/ Jammu
AA Cost (Rs. In Lakh)	50.00
Total cost of completion/Exp. Incurred ending 3/2022	34.66(lac)
Date of Start (Month/Year)	Feb-22
Date of Completion (Month/Year)	25-03-2022
No. of beneficiaries	7500






S.No	105
Name of the work with Location	Const. of Concrete Basket Ball at GHSS Sunjwan
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Gandhi Nagar/ Jammu
AA Cost (Rs. In Lakh)	15.00
Total cost of completion/Exp. Incurred ending 3/2022	7.50(lac)
Date of Start (Month/Year)	Feb-22
Date of Completion (Month/Year)	25-03-2022
No. of beneficiaries	7500

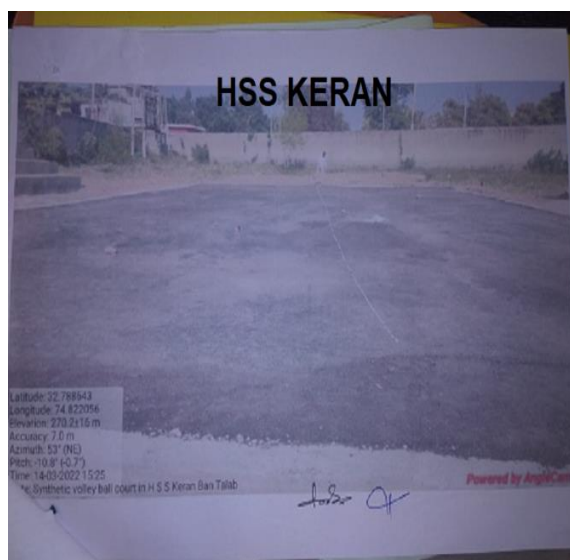


S.No	106
Name of the work with Location	Const. of Syn. Volley Ball Court at Govt Boys PG Pahri Hostel Keran
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Bhalwal/ Jammu
AA Cost (Rs. In Lakh)	14.58
Total cost of completion/Exp. Incurred ending 3/2022	8.59(LAC)
Date of Start (Month/Year)	Feb-22
Date of Completion (Month/Year)	26-03-2022
No. of beneficiaries	1500



S.No	107
Name of the work with Location	Const. of concrete Badminton Court at HS Quasim Nagar
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Gandhi Nagar/ Jammu
AA Cost (Rs. In Lakh)	4.50(lac)
Total cost of completion/Exp. Incurred ending 3/2022	2.13
Date of Start (Month/Year)	Jan-22
Date of Completion (Month/Year)	Mar-22
No. of beneficiaries	500

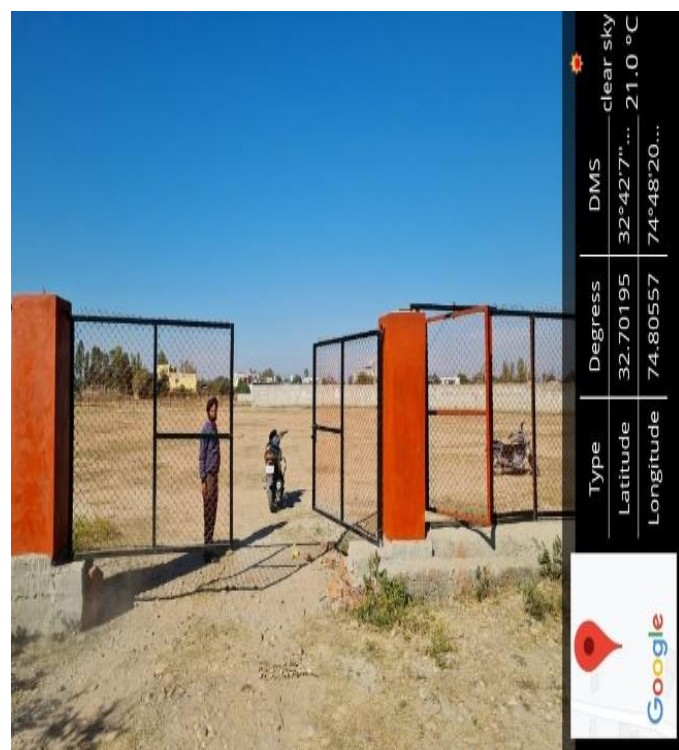

S.No	108
Name of the work with Location	Const. of Cricket Wicket Net at Phallian Mandal
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	satwari/ Jammu
AA Cost (Rs. In Lakh)	49.18
Total cost of completion/Exp. Incurred ending 3/2022	18.18900(lac)
Date of Start (Month/Year)	Jan-22
Date of Completion (Month/Year)	Completed
No. of beneficiaries	5000

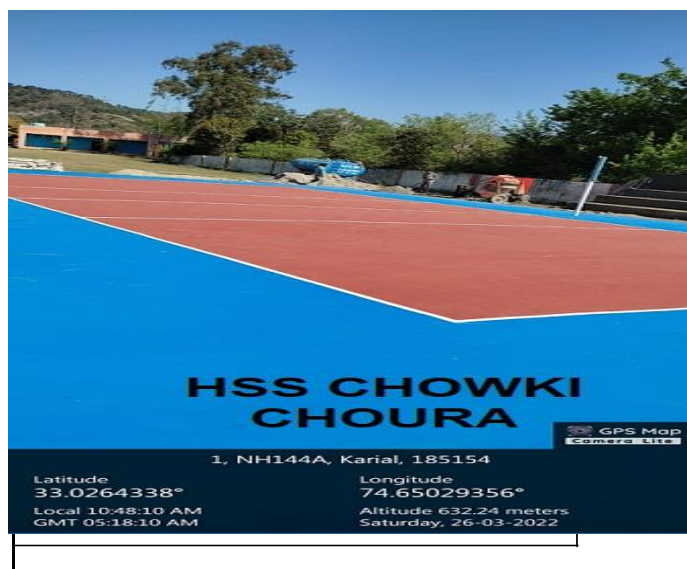



S.No	109
Name of the work with Location	Const. of Syn. Volley Ball Court at HSS ChowkiChoura
Department/Organization	YSS/Directorate of YSS
Executive Agency	Ex En JK Sports Council J/K
Block District	Jourian/ Jammu
AA Cost (Rs. In Lakh)	15.5
Total cost of completion/Exp. Incurred ending 3/2022	9.21300(LAC)
Date of Start (Month/Year)	Feb-22
Date of Completion (Month/Year)	30-03-2022
No. of beneficiaries	2000


<p>Kas Balari Unnamed Road, Kas Balari, 185211 Lat N 33° 37' 57.7704" Long E 74° 9' 2.646" 09/03/22 09:40 AM</p>	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of Completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>110 Development of playfield at GMS Kundbehra YSS/Directorate of YSS RDD Mendhar/Poonch 7.00 6.99 2020-21 31-03-2022 700</p>
--	--	---


<p>Latitude: 33.0264338° Longitude: 74.65029356° Altitude: 632.24 meters Local: 10:48:10 AM GMT: 05:18:10 AM Date: 26-03-2022 Time: 10:48:10 AM GPS: 33.0264338, 74.65029356</p>	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>111 Development of playfield at GPS Mohalla Kashmerian YSS/Directorate of YSS RDD Mendehar/Poonch 5.50 5.50 2020-21 31-03-2022 600</p>
--	--	---





	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>112 Development of playfield at MS TherpurSalwah * YSS/Directorate of YSS  RDD  Mendhar/Poonch  4.96  1.56  2020-21 31-03-2022  500</p>
---	--	--

	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>113 Construction of synthetic Kho-Kho playfield at HSS SalwahMendhar YSS/Directorate of YSS RDD Mendhar/Poonch 8.00  7.93 2020-21 31-03-2022 1000</p>
--	--	--

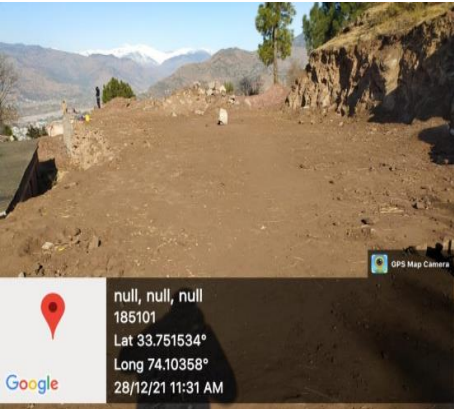
	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>114 Development of playfield at Primary School Dhamal Upper Kanuyian YSS/Directorate of YSS RDD Poonch/Poonch 2.80  1.16 2020-21 31-03-2022 500</p>
---	--	--

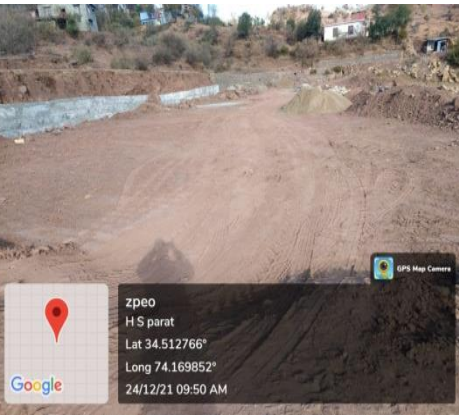
	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>115 Development of playfield at Govt. HS Parat YSS/Directorate of YSS RDD MendharPoonch 5.40  2.70 2020-21 31-03-2022 800</p>
---	--	--

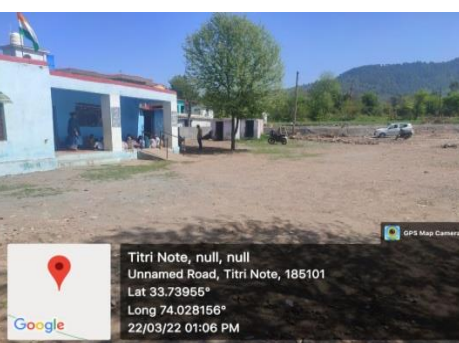
	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>116 Development of playfield at Govt. Primary School Floor YSS/Directorate of YSS RDD Poonch/Poonch 10.00  6.35 2020-21 31-03-2022 800</p>
--	--	---


	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure Incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>117 Development of playfield at Govt. MS Dharana YSS/Directorate of YSS RDD Mendhar/Poonch 5.00  2.976 2020-21 31-03-2022 500</p>
	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>118 Development of playfield at Govt. MS Mangnar YSS/Directorate of YSS RDD Poonch/POOnch 3.98  2.38 2020-21 31-03-2022 600</p>
	<p>S.No Name of the work with Location  Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>119 Construction of playfield at Colony W.No 01 Pyt. BhuratiBalakote  YSS/Directorate of YSS  RDD  Balakote/Poonch 10.00  2.61 2020-21 31-03-2022 800</p>





	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>120 Development of playfield at MS Dheri YSS/Directorate of YSS RDD Mendhar/Poonch 2.80 1.33 2020-21 31-03-2022 500</p>
---	--	--


	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>121 Development of playfield at MS Lie Bhatidhar YSS/Directorate of YSS RDD Mendhar/Poonch 7.00 2.97 2020-21 31-03-2022 1000</p>
--	--	---


	<p>S.No Name of the work with Location Department/Organization Executive Agency Block/District AA Cost (Rs. In lakhs) Total Cost of completion/Expenditure incurred ending 03/2022. Date of start (Month/Year) Date of completion (Month) No. of beneficiaries</p>	<p>122 Development of playfield at MS Chattral YSS/Directorate of YSS RDD Mendhar/Poonch 15.00 2.50 Sept, 21 Mar, 22 1500</p>
---	--	---

	S.No	123
	Name of the work with Location	Development of playfield at Govt. PS Manda Gursai
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Mendhar/Poonch
	AA Cost (Rs. In lakhs)	20.00
	Total Cost of completion/Expenditure incurred ending 03/2022.	10.00
	Date of start (Month/Year)	Aug 2021
	Date of completion (Month)	Mar, 22
	No. of beneficiaries	1200


	S. No.	124
	Name of the Work with Location	Construction of Boundary Wall, Badminton Posts, Kho-Kho Poles at Govt. UPS Jabba Gool, Ramban
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	PWD
	Block /District	Ramban
	AA Cost Rs. In Lacs	10.81
	Total Cost of Completion/Expenditure incurred ending 03/2022	8.37
	Date of Start of(Month/Year )	Oct-21
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	600


	S. No.	125
	Name of the Work with Location	Construction of Concrete Badminton Court at HS Permote by way of earth cutting
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	PWD
	Block /District	Permote
	AA Cost Rs. In Lacs	8.40
	Total Cost of Completion/Expenditure incurred ending 03/2022	2.81
	Date of Start of(Month/Year )	Jan-22
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	300


	Sr. No.	126
	Name of the work with Location	Dev. of Play Field at H/S Gundi
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Khawas/ Rajouri
	AA Cost (Rs. In lakhs)	1.97
	Total Cost of Completion/Expenditure incurred ending 3/2022	1.97
	Date of Start (Month/Year)	Feb, 22
	Date of Completion (Month/Year)	Mar, 22
	No. of beneficiaries	240

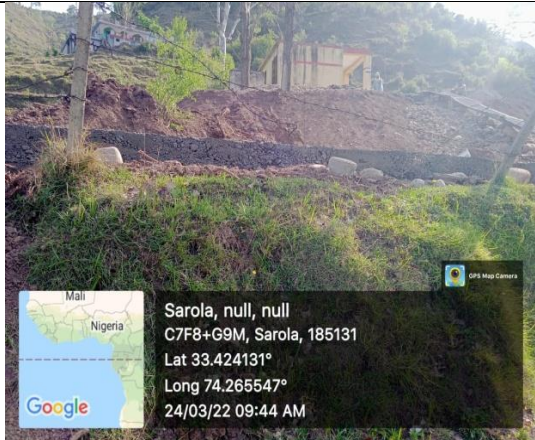
	Sr. No.	127
	Name of the work with Location	Dev. of Play Field at M/S Katarmal
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Panjgrain/ Rajouri
	AA Cost (Rs. In lakhs)	2.46
	Total Cost of Completion/Expenditure incurred ending 3/2022	2.46
	Date of Start (Month/Year)	Feb, 22
	Date of Completion (Month/Year)	Mar, 22
	No. of beneficiaries	170



	Sr. No.	128
	Name of the work with Location	Dev. of Play Field at H/S Hayatpura
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Manjakote/ Rajouri
	AA Cost (Rs. In lakhs)	1.40
	Total Cost of Completion/Expenditure incurred ending 3/2022	1.40
	Date of Start (Month/Year)	Feb, 22
	Date of Completion (Month/Year)	Mar, 22
	No. of beneficiaries	220

	Sr. No.	129
	Name of the work with Location	Dev. of Play Field M/S Doongi
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Doongi/ Rajouri
	AA Cost (Rs. In lakhs)	2.40
	Total Cost of Completion/Expenditure incurred ending 3/2022	2.40
	Date of Start (Month/Year)	Feb, 22
	Date of Completion (Month/Year)	Mar, 22
	No. of beneficiaries	145

	S.No	130
	Name of the work with location	Repair/Renovation of newly occupied Dis Budgam.
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Budgam
	AA Cost (Rs. in Lakhs)	11.87
	Total Cost of completion/Expenditure incurred ending 03/2022	11.510
	Date of Start (Month/Year)	Jun-21
	Date of completion(Month/Year)	Mar-22
	No. of beneficiaries	DYSSO Budgam

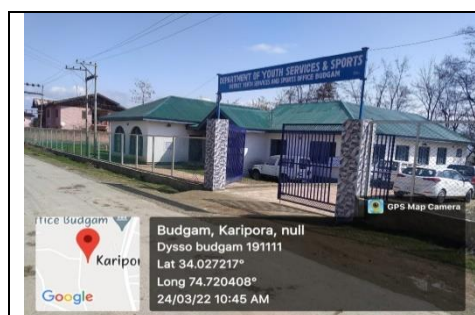


S.No	131
Name of the work with location	Chainlink Fencing/walling of newly occupied office Budgam.
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Budgam
AA Cost (Rs. in Lakhs)	11.40
Total Cost of completion/Expenditure incurred ending 03/2022	11.026
Date of Start (Month/Year)	Jul-21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	DYSSO Budgam




S.No	132
Name of the work with location	Panelling/Flooring of hall, tiles for corridor in newly occupied building at DYSSO Budgam.
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Budgam
AA Cost (Rs. in Lakhs)	6.95
Total Cost of completion/Expenditure incurred ending 03/2022	4.06
Date of Start (Month/Year)	Jan-22
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	DYSSO Budgam



S.No	133
Name of the work with location	Chain link fencing around Synthetic Football field Soibugh JKIDFC funding
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Soibugh/Budgam
AA Cost (Rs. in Lakhs)	2.72
Total Cost of completion/Expenditure incurred ending 03/2022	2.66
Date of Start (Month/Year)	Dec-21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	450

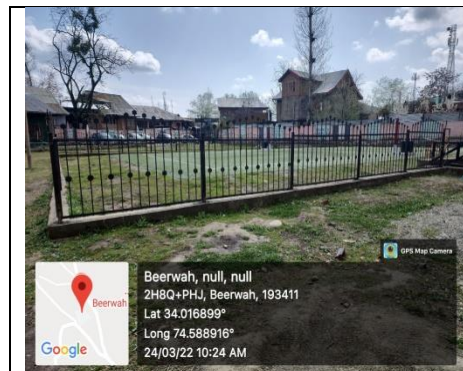


S.No	134
Name of the work with location	Chain link fencing around Syn Beerwah JKIDFC funding
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Beerwa/Budgam
AA Cost (Rs. in Lakhs)	1.97
Total Cost of completion/Expenditure incurred ending 03/2022	1.95
Date of Start (Month/Year)	Mar-22
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	350

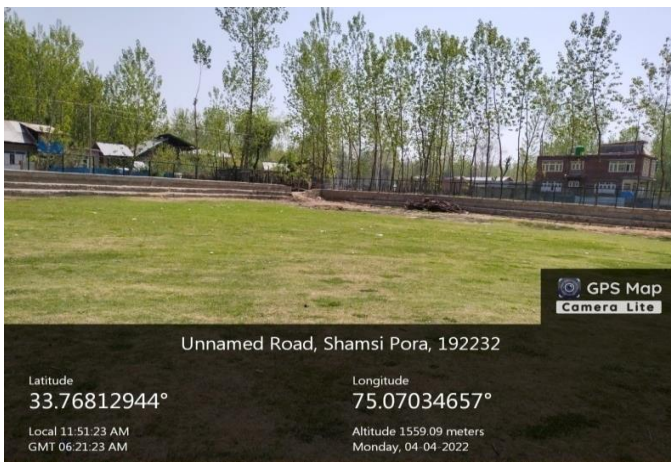


Sr. No.	135
Name of the work with Location	Dev. Of playfield at NowporaKharpora BWO fencing, filling, levelling & seating arrangements
Department/Organization	YSS/Directorate of YSS
Executive Agency	Rural Development Department
Block/District	Qaimoh/Kulgam
AA Cost(Rs. In lacs)	14.93
Total Cost of completion/Expenditure incurred ending 03/2022	9.90/9.90
Date of Start(Month/Year)	Oct-21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	2,000




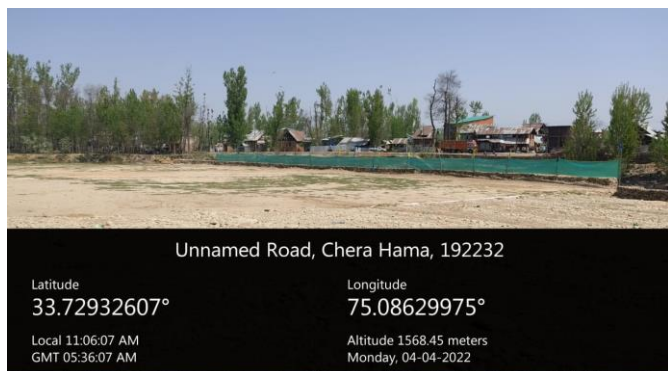

Sr. No.	136
Name of the work with Location	Dev. Of playfield at Redwani BWO protection wall and levelling
Department/Organization	Youth Services and Sports
Executive Agency	Rural Development Department
Block/District	Qaimoh/Kulgam
AA Cost(Rs. In lacs)	9.25
Total Cost of completion/Expenditure incurred ending 03/2022	5.42/5.42
Date of Start(Month/Year)	Oct-21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	1,000

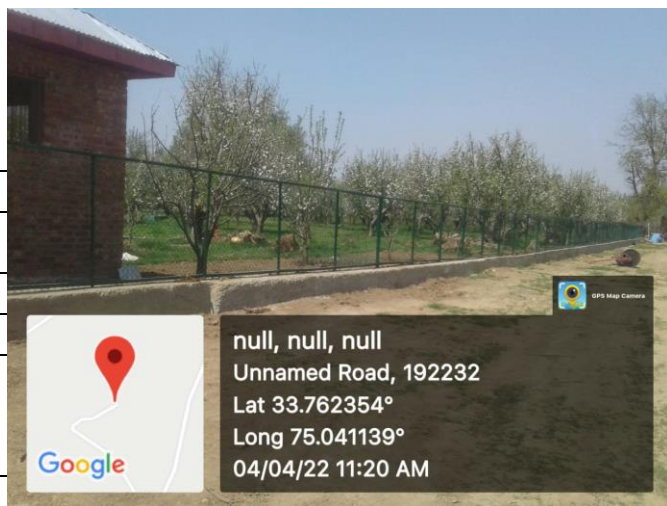

Sr. No.	137
Name of the work with Location	Dev. Of playfield at Frisal BWO chainlink fencing Gate and cricket wicket
Department/Organization	YSS/Directorate of YSS
Executive Agency	Rural Development Department
Block/District	Frisal/Kulgam
AA Cost(Rs. In lacs)	15.33
Total Cost of completion/Expenditure incurred ending 03/2022	8.83/8.83
Date of Start(Month/Year)	Oct-21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	10,000

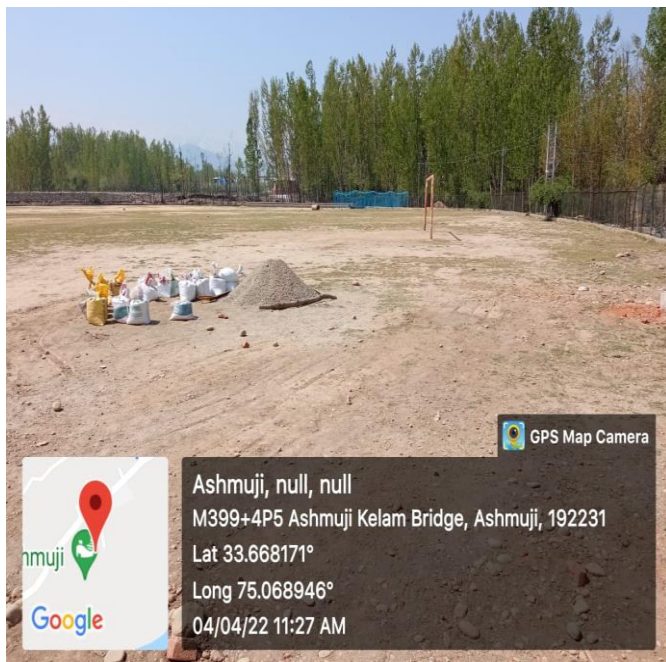


<b>Sr. No.</b>	<b>138</b>
<b>Name of the work with Location</b>	<b>Dev. Of playfield at Sports Stadium Ashmuji BWO cricket wicket &amp; const. of Gate</b>
<b>Department/Organization</b>	<b>YSS/Directorate of YSS</b>
<b>Executive Agency</b>	<b>Rural Development Department</b>
<b>Block/District</b>	<b>Qaimoh/Kulgam</b>
<b>AA Cost(Rs. In lacs)</b>	<b>5.00</b>
<b>Total Cost of completion/Expenditure incurred ending 03/2022</b>	<b>4.21/4.21</b>
<b>Date of Start(Month/Year)</b>	<b>Oct-21</b>
<b>Date of completion(Month/Year)</b>	<b>Mar-22</b>
<b>No. of beneficiaries</b>	<b>10,000</b>



<b>Sr. No.</b>	<b>139</b>
<b>Name of the work with Location</b>	<b>Dev. Of playfield at Sports Stadium Behibagh BWO cricket wicket &amp; const. of Gate</b>
<b>Department/Organization</b>	<b>YSS/Directorate of YSS</b>
<b>Executive Agency</b>	<b>Rural Development Department</b>
<b>Block/District</b>	<b>Behibagh/Kulgam</b>
<b>AA Cost(Rs. In lacs)</b>	<b>5.50</b>
<b>Total Cost of completion/Expenditure incurred ending 03/2022</b>	<b>3.55/3.55</b>
<b>Date of Start(Month/Year)</b>	<b>Oct-21</b>
<b>Date of completion(Month/Year)</b>	<b>Mar-22</b>
<b>No. of beneficiaries</b>	<b>14,000</b>



<b>Sr. No.</b>	<b>140</b>
<b>Name of the work with Location</b>	<b>Dev. Of playfield at MS Momindangi part(A+B+C+D+E) *</b>
<b>Department/Organization</b>	YSS/Directorate of YSS
<b>Executive Agency</b>	<b>Rural Development Department</b>
<b>Block/District</b>	<b>Bijbehara/Anantnag</b>
<b>AA Cost(Rs. In lacs)</b>	<b>14.68</b>
<b>Total Cost of completion/Expenditure incurred ending 03/2022</b>	<b>14.68/14.68</b>
<b>Date of Start(Month/Year)</b>	<b>Apr-15</b>
<b>Date of completion(Month/Year)</b>	<b>Mar-22</b>
<b>No. of beneficiaries</b>	<b>3,000</b>

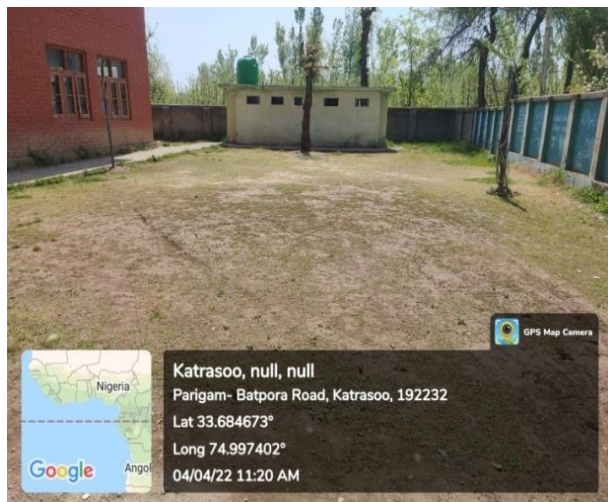

<b>Sr. No.</b>	<b>141</b>
<b>Name of the work with Location</b>	<b>Dev. Of playfield at BHS Katrasoo</b>
<b>Department/Organization</b>	YSS/Directorate of YSS
<b>Executive Agency</b>	<b>Rural Development Department</b>
<b>Block/District</b>	<b>Kulgam/Kulgam</b>
<b>AA Cost(Rs. In lacs)</b>	<b>2.68</b>
<b>Total Cost of completion/Expenditure incurred ending 03/2022</b>	<b>2.68/1.68</b>
<b>Date of Start(Month/Year)</b>	<b>Apr-18</b>
<b>Date of completion(Month/Year)</b>	<b>Mar-22</b>
<b>No. of beneficiaries</b>	<b>2,000</b>






<b>Sr. No.</b>	<b>142</b>
<b>Name of the work with Location</b>	<b>Dev. Of playfield near MS Khrewan BWO of Seating arrangement, filling &amp; other allied works</b>
<b>Department/Organization</b>	YSS/Directorate of YSS
<b>Executive Agency</b>	<b>Rural Development Department</b>
<b>Block/District</b>	<b>Qaimoh/Kulgam</b>
<b>AA Cost(Rs. In lacs)</b>	<b>13.00</b>
<b>Total Cost of completion/Expenditure incurred ending 03/2022</b>	<b>9.00/8.6105</b>
<b>Date of Start(Month/Year)</b>	<b>Apr-20</b>
<b>Date of completion(Month/Year)</b>	<b>Mar-22</b>
<b>No. of beneficiaries</b>	<b>5,000</b>





<b>Sr. No.</b>	<b>143</b>
<b>Name of the work with Location</b>	<b>Maintenance /face lifting of main building in stadium</b>
<b>Department/Organization</b>	YSS/Directorate of YSS
<b>Executive Agency</b>	Ex En JK Sports Council J/K
<b>Block/District</b>	GCOPE/ Ganderbal
<b>AA Cost (Rs. In lakhs)</b>	5.85
<b>Total Cost of Completion/Expenditure incurred ending 3/2022</b>	5.81
<b>Date of Start (Month/Year)</b>	Sept, 21
<b>Date of Completion (Month/Year)</b>	Feb-22
<b>No. of beneficiaries</b>	




<b>Sr. No.</b>	<b>144</b>
<b>Name of the work with Location</b>	<b>Construction of Cricket pitch</b>
<b>Department/Organization</b>	YSS/Directorate of YSS
<b>Executive Agency</b>	Ex En JK Sports Council J/K
<b>Block/District</b>	GCOPE/ Ganderbal
<b>AA Cost (Rs. In lakhs)</b>	4.91
<b>Total Cost of Completion/Expenditure incurred ending 3/2022</b>	4.73
<b>Date of Start (Month/Year)</b>	Sept, 21
<b>Date of Completion (Month/Year)</b>	Feb-22
<b>No. of beneficiaries</b>	

 <p> <small>           Address: GCOPE, 2012            Longitude: 14.7196            Latitude: 122.494            Altitude: 5.0m            Time: 04/04/2022 15:45            Photo: Main Administrative Building         </small> </p>	Sr. No.	145
	Name of the work with Location	Face lifting of main administrative building at GCOPE
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	Ex En JK Sports Council J/K
	Block/District	GCOPE/ Ganderbal
	AA Cost (Rs. In lakhs)	7.50
	Total Cost of Completion/Expenditure incurred ending 3/2022	6.53
	Date of Start (Month/Year)	Sept, 21
	Date of Completion (Month/Year)	Mar-22
	No. of beneficiaries	

 <p> <small>           Address: GCOPE, 2012            Longitude: 14.7196            Latitude: 122.494            Altitude: 5.0m            Time: 04/04/2022 15:45            Photo: Synthetic volleyball court         </small> </p>	Sr. No.	146
	Name of the work with Location	Development of synthetic volleyball court at GCOPE
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	Ex En JK Sports Council J/K
	Block/District	GCOPE/ Ganderbal
	AA Cost (Rs. In lakhs)	12.61
	Total Cost of Completion/Expenditure incurred ending 3/2022	9.24
	Date of Start (Month/Year)	Sept, 21
	Date of Completion (Month/Year)	Feb-22
	No. of beneficiaries	

 <p> <b>District Youth Services and Sports Office Pulwama</b>  <b>Detail of work completed under state sector 2021-22</b> </p> <p> <small>           null, null, null            Unnamed Road, 191103            Lat 34.044544°            Long 75.071238°            01/04/22 05:04 PM         </small> </p>	S.No	147
	Name of the work with location	Development of Playfield at Satoora
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Aripal / Pulwama
	AA Cost (Rs. in Lakhs)	15.00
	Total Cost of completion/Expenditure incurred ending 03/2022	10.77
	Date of Start (Month/Year)	Aug-21
	Date of completion(Month/Year)	Mar-22
	No. of beneficiaries	3000


	Sr .NO	148
	Name of work with Location	Construction of Path repairment of manholes & filing Bathrooms of Office at Wazir Bagh Srinagar
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	Project Engineer, SICOP Srinagar
	Block/District	Srinagar
	AA Cost(Rs in Lakhs)	9.92 lacs
	Total Cost of completion/Expenditure incurred ending 03/2022	9.92/9.92
	Date of Start(Month/Yes)	April, 21
	Date of Completion(Month/Year)	Aug, 21
	No of Beneficiaries.	

	Sr .NO	149
	Name of work with Location	Construction of Synthetic Volleyball Court at BHSS GulabBagh, Srinagar
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	R&B Department
	Block/District	Srinagar
	AA Cost(Rs in Lakhs)	12.26 Lacs
	Total Cost of completion/Expenditure incurred ending 03/2022	12.26 Lacs
	Date of Start(Month/Yes)	Oct, 2021
	Date of Completion(Month/Year)	Dec, 2021
	No of Beneficiaries.	700







Sr .NO	150
Name of work with Location	Construction of Concrete work of Path/Parking area infront of Directorate Office Complex
Department/Organisation	YSS/Directorate of YSS
Executive Agency	Project Engineer, SICOP Srinagar
Block/District	Srinagar
AA Cost(Rs in Lakhs)	15.44 Lacs
Total Cost of completion/Expenditure incurred ending 03/2022	15.44 Lacs / 8.00 Lacs
Date of Start(Month/Yes)	Oct, 21
Date of Completion(Month/Year)	Dec,21
No of Beneficiaries.	

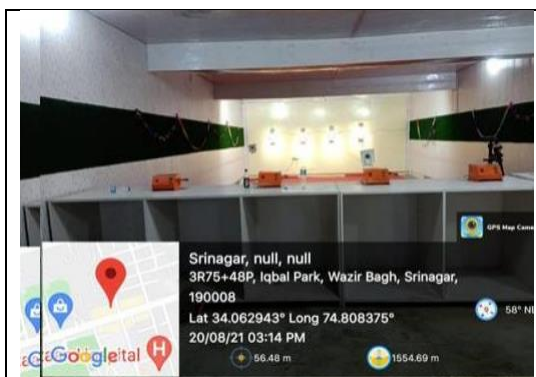

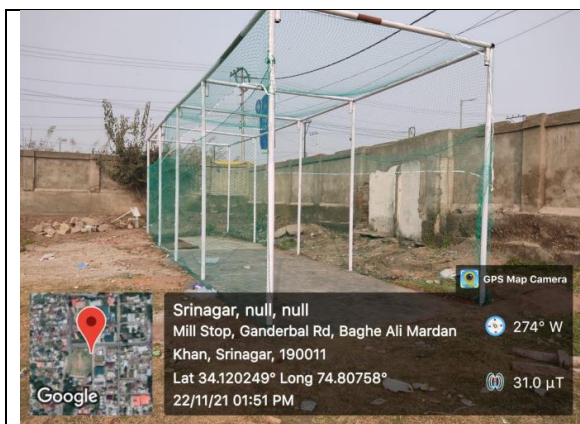

Sr .NO	1 5 1
Name of work with Location	Construction of Indoor Shooting Hall at Youth Hostel Wazir Bagh Srinagar
Department/Organisation	YSS/Directorate of YSS
Executive Agency	Project Engineer, SICOP Srinagar
Block/District	Srinagar
AA Cost(Rs in Lakhs)	4.67 Lacs
Total Cost of completion/Expenditure incurred ending 03/2022	4.67 Lacs
Date of Start(Month/Yes)	Aug, 21
Date of Completion(Month/Year)	Sept,21
No of Beneficiaries.	300





Sr .NO	152
Name of work with Location	Construction of Cricket Wicket Net (Practice Pitch) at Govt. BHSS ZadibalSgr
Department/Organisation	YSS/Directorate of YSS
Executive Agency	R&B Department
Block/District	Srinagar
AA Cost(Rs in Lakhs)	2.93 Lacs
Total Cost of completion/Expenditure incurred ending 03/2022	2.93 Lacs
Date of Start(Month/Yes)	Oct, 21
Date of Completion(Month/Year)	Dec, 21
No of Beneficiaries.	900

	Sr .NO	153
	Name of work with Location	Chainlink fencing around Synthetic Volleyball Court constructed at BHS Lawaypora through JKIDFC funding
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	R&B Department
	Block/District	Srinagar
	AA Cost(Rs in Lakhs)	8.00 Lacs
	Total Cost of completion/Expenditure incurred ending 03/2022	8.00 Lacs
	Date of Start(Month/Yes)	Jan, 22
	Date of Completion(Month/Year)	Feb, 22
	No of Beneficiaries.	450


	Sr .NO	154
	Name of work with Location	Construction of Synthetic badminton Court at BHSS Shalimar
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	R&B Department
	Block/District	Srinagar
	AA Cost(Rs in Lakhs)	11.17
	Total Cost of completion/Expenditure incurred ending 03/2022	11.17
	Date of Start(Month/Yes)	Sept, 21
	Date of Completion(Month/Year)	Mar-22
	No of Beneficiaries.	200

	Sr .NO	155
	Name of work with Location	Chainlink fencing around Synthetic Volleyball Court constructed at GHSS Kothibagh through JKIDFC funding
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	R&B Department
	Block/District	Srinagar
	AA Cost(Rs in Lakhs)	8.00
	Total Cost of completion/Expenditure incurred ending 03/2022	5.00
	Date of Start(Month/Yes)	Sept, 21
	Date of Completion(Month/Year)	Mar-22
	No of Beneficiaries.	150

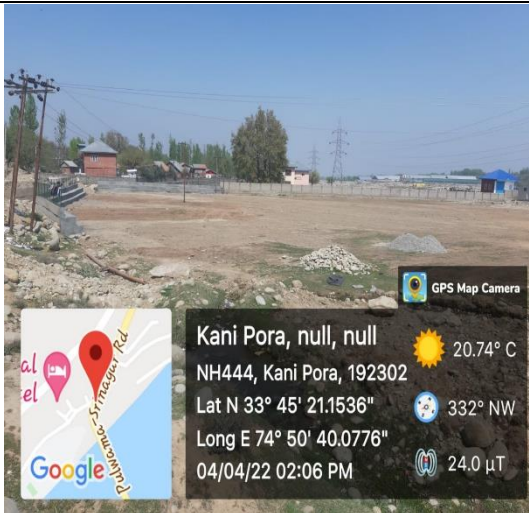
	S. No	156
	Name of the Work with Location	Name of the Work with Location: Dev of Play field at SindoShirmal opposite Army Goodwill School Shopian
	Department/Organization:	YSS/Directorate of YSS
	Executive Agency :	ACD Shopian
	Block /District :	Shopian
	AA Cost Rs. In Lacs:	26.61
	Total Cost of Completion	15.24
	Date of Start of(Month/Year )	July, 21
	Date of Completion (Month/Year)	Jan,22
	No of Beneficiaries	3000

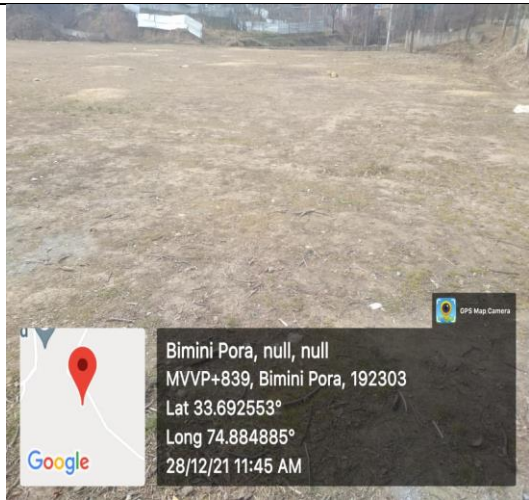
	S. No	157
	Name of the Work with Location	Development of Playfield at Open Playfield at Bemnipora (Batnad) by way of levelling, filling and fencing
	Department/Organization:	YSS/Directorate of YSS
	Executive Agency :	ACD Shopian
	Block /District :	Ramnagri / Shopian
	AA Cost Rs. In Lacs:	4.37
	Total Cost of Completion	3.37
	Date of Start of(Month/Year )	July, 21
	Date of Completion (Month/Year)	Mar, 22
	No of Beneficiaries	5000



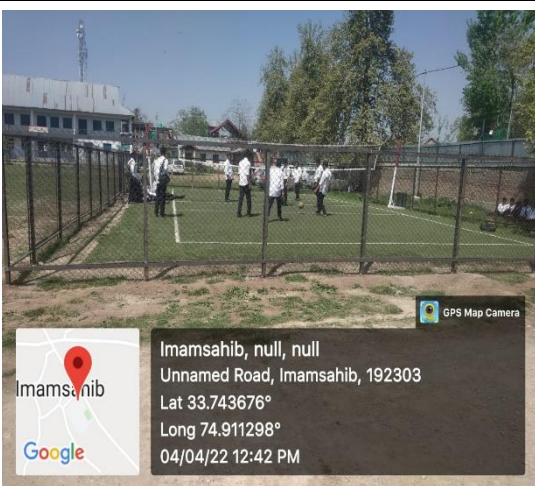


	S. No	158
	Name of the Work with Location	Chainlink fencing around Synthetic Volleyball Court constructed at HSS Imam Sahib through JKIDFC funding
	Department/Organization:	YSS/Directorate of YSS
	Executive Agency :	ACD Shopian
	Block /District :	Imamsahib / Shopian
	AA Cost Rs. In Lacs:	3.05
	Total Cost of Completion	2.57
	Date of Start of(Month/Year )	Nov, 21
	Date of Completion (Month/Year)	Mar, 22
	No of Beneficiaries	1500

	S. No	159
	Name of the Work with Location	Chainlink fencing around Synthetic Volleyball Court constructed at HSS Sedow through JKIDFC funding
	Department/Organization:	YSS/Directorate of YSS
	Executive Agency :	ACD Shopian
	Block /District :	Ramnagri / Shopian
	AA Cost Rs. In Lacs:	3.05
	Total Cost of Completion	2.63
	Date of Start of(Month/Year )	Nov, 21
	Date of Completion (Month/Year)	Mar, 22
	No of Beneficiaries	1500

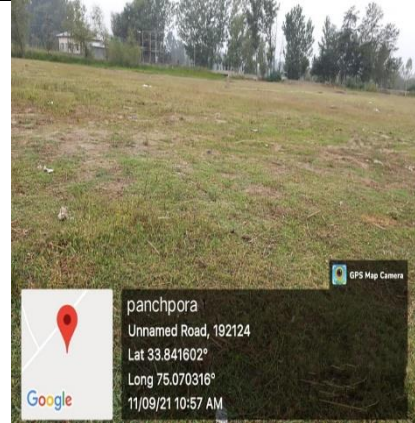	S. No.	160
	Name of the Work with Location	Development of Playfield at Krad *
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Achabal/Anantnag
	AA Cost Rs. In Lacs	19.65
	Total Cost of Completion/Expenditure incurred ending 03/2022	19.65
	Date of Start of(Month/Year ) 07/2022	Oct 16
Date of Completion (Month/Year)		Mar, 22
No of Beneficiaries		15000

	S. No.	161
	Name of the Work with Location	<i>Development of Playfield at Panchpora *</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	<i>Bijbehara/Anantnag</i>
	AA Cost Rs. In Lacs	<i>26.08</i>
	Total Cost of Completion/Expenditure incurred ending 03/2022	<i>26.08</i>
	Date of Start of(Month/Year ) 07/2022	<i>Mar, 17</i>
Date of Completion (Month/Year)		<i>Mar, 22</i>
No of Beneficiaries		<i>8000</i>

 <p>govt middle school panard. panchayat halqa khiram dargah.</p> <div data-bbox="203 634 381 745">  </div> <div data-bbox="397 634 803 745"> <p><b>Khiram</b> Khidam Internal Road, 192401 Lat N 33° 52' 55.1316" Long E 75° 11' 7.8432" 24/03/21 10:56 AM</p> </div>	S. No.	162
	Name of the Work with Location	<i>Development of Playfield at MS Panard *</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Bijbehara/Anantnag
	AA Cost Rs. In Lacs	20.59
	Total Cost of Completion/Expenditure incurred ending 03/2022	20.59
	Date of Start of(Month/Year )	Nov. 17
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	8000


 <div data-bbox="203 1375 332 1501">  </div> <div data-bbox="349 1375 673 1501"> <p>null, null, null Unnamed Road, 192125 Lat N 33° 48' 15.1164" Long E 75° 16' 52.5036" 04/08/21 10:49 AM</p> </div> <div data-bbox="560 1344 673 1501"> <p>GPS Map Camera 23.25° C 227° SW 25.0 μT</p> </div>	S. No.	163
	Name of the Work with Location	<i>Development of Playfield at MS Ashidar *</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Bijbehara/Anantnag
	AA Cost Rs. In Lacs	14.69
	Total Cost of Completion/Expenditure incurred ending 03/2022	14.69
	Date of Start of(Month/Year )	May 17
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	7500






**Panchayat Halqa Marhama A**

S. No.	164
Name of the Work with Location	<i>Development of Playfield at MS Marhama*</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	Bijbehara/Anantnag
AA Cost Rs. In Lacs	11.66
Total Cost of Completion/Expenditure incurred ending 03/2022	11.66
Date of Start of(Month/Year )	Nov 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	4500

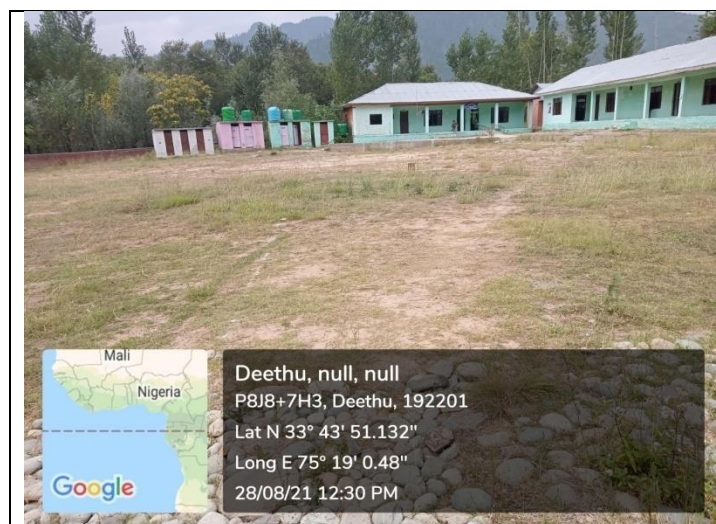

S. No.	165
Name of the Work with Location	<i>Development of Playfield at MS Yanner *</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	Edu Deptt
Block /District	K.Pora/Anantnag
AA Cost Rs. In Lacs	13.98
Total Cost of Completion/Expenditure incurred ending 03/2022	13.98
Date of Start of(Month/Year )	July 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	4000

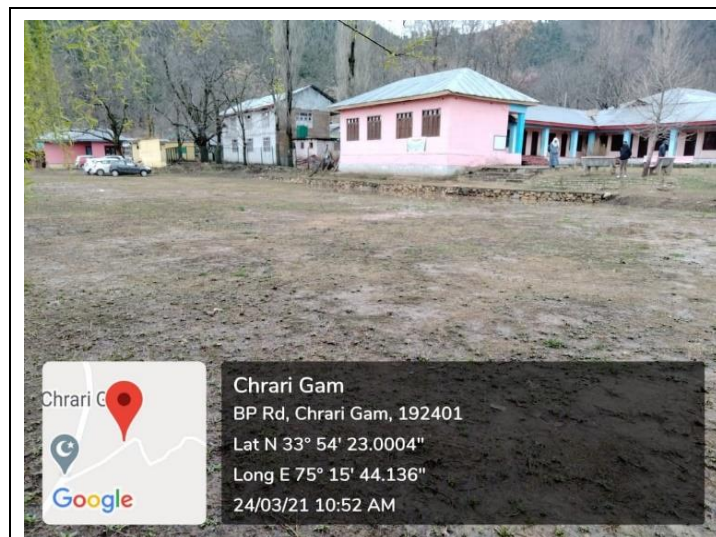

S. No.	166
Name of the Work with Location	<i>Development of Playfield at Hardukishroo *</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	K.Pora/Anantnag
AA Cost Rs. In Lacs	19.27
Total Cost of Completion/Expenditure incurred ending 03/2022	19.27
Date of Start of(Month/Year )	Aug 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	5500



S. No.	168
Name of the Work with Location	<i>Development of Playfield at Tarbal *</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	Bijbehara / Anantnag
AA Cost Rs. In Lacs	10.00
Total Cost of Completion/Expenditure incurred ending 03/2022	10.00
Date of Start of(Month/Year )	Nov 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	8500




S. No.	168
Name of the Work with Location	<i>Development of Playfield at MS AhooPaison *</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	Shangus / Anantnag
AA Cost Rs. In Lacs	5.98
Total Cost of Completion/Expenditure incurred ending 03/2022	5.98
Date of Start of(Month/Year )	Oct 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	4400



S. No.	169
Name of the Work with Location	<i>Development of Playfield at HS Posh Kreeri*</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	K. Pora / Anantnag
AA Cost Rs. In Lacs	7.83
Total Cost of Completion/Expenditure incurred ending 03/2022	7.83
Date of Start of(Month/Year )	Oct 17
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	4500




	S. No.	170
	Name of the Work with Location	<i>Development of Playfield at Jablipora *</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Bijbehara / Anantnag
	AA Cost Rs. In Lacs	1.20
	Total Cost of Completion/Expenditure incurred ending 03/2022	1.20
	Date of Start of(Month/Year )	Nov 17
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	5500

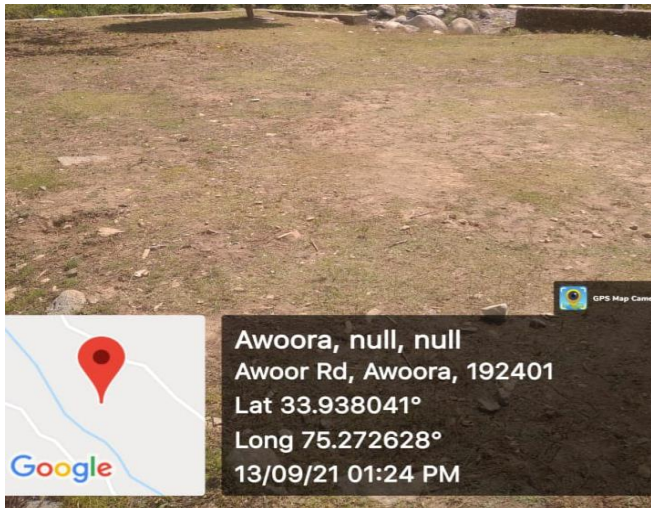
	S. No.	171
	Name of the Work with Location	<i>Development of Playfield at Overa ST *</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Pahalgam / Anantnag
	AA Cost Rs. In Lacs	14.96
	Total Cost of Completion/Expenditure incurred ending 03/2022	14.96
	Date of Start of(Month/Year )	Nov 17
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	5500




S. No.	172
Name of the Work with Location	<i>Development of Playfield at Sotki Pora*</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	D. Pora / Anantnag
AA Cost Rs. In Lacs	11.23
Total Cost of Completion/Expenditure incurred ending 03/2022	11.23
Date of Start of (Month/Year )	Nov 18
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	5600

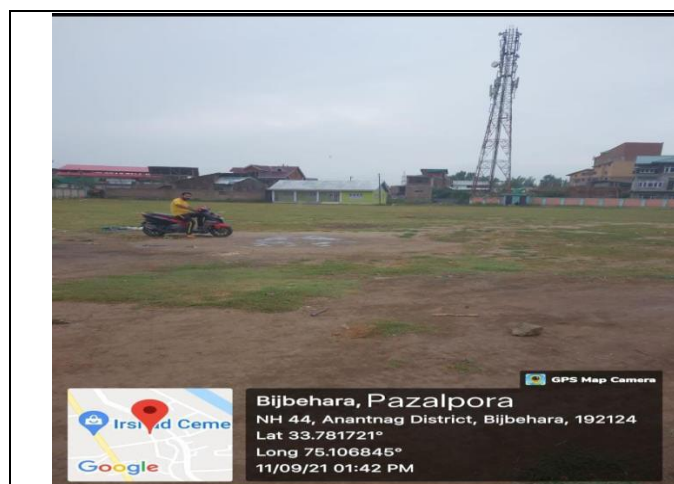

S. No.	173
Name of the Work with Location	<i>Development of Playfield at MS Pazalpura *</i>
Department/Organization	YSS/Directorate of YSS
Executive Agency	RDD
Block /District	Bijbehara / Anantnag
AA Cost Rs. In Lacs	8.80
Total Cost of Completion/Expenditure incurred ending 03/2022	8.80
Date of Start of (Month/Year )	Nov 18
Date of Completion (Month/Year)	Mar-22
No of Beneficiaries	6500


	S. No.	174
	Name of the Work with Location	<i>Development of Playfield atCheniGundkanelwan</i>
	Department/Organization	YSS/Directorate of YSS
	Executive Agency	RDD
	Block /District	Bijbehara / Anantnag
	AA Cost Rs. In Lacs	19.00
	Total Cost of Completion/Expenditure incurred ending 03/2022	12.61
	Date of Start of(Month/Year )	Nov, 21
	Date of Completion (Month/Year)	Mar-22
	No of Beneficiaries	5600

	Sr .NO	175
	Name of work with Location	Dev. of Play field at Allama Anwar Shah Stadium (RA) at KuligamLollab.
	Department/Organisation	YSS/Directorate of YSS
	Executive Agency	RDD
	Block/District	Wavoor
	AA Cost(Rs in Lakhs)	20.00
	Total Cost of completion/Expenditure incurred ending 03/2022	9.09
	Date of Start(Month/Yes)	Nov-21
	Date of Completion(Month/Year)	Mar-22
	No of Beneficiaries	5000







Sr .NO	176
Name of work with Location	Development of playfield Kindergarten at Hirripayeen.
Department/Organisation	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Qadriabad /Kupwara
AA Cost(Rs in Lakhs)	3.00
Total Cost of completion/Expenditure incurred ending 03/2022	2.28
Date of Start(Month/Yes)	Dec,21
Date of Completion(Month/Year)	Mar, 22
No of Beneficiaries.	3000

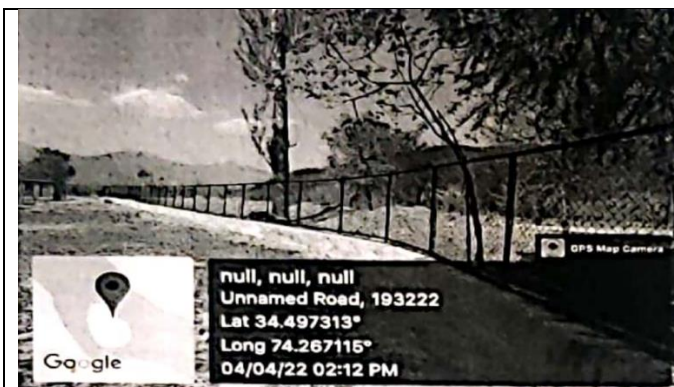

Sr .NO	177
Name of work with Location	Development of Playfield at BHSS HatmullaHandwara by way of fencing
Department/Organisation	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Kupwara
AA Cost(Rs in Lakhs)	11.94
Total Cost of completion/Expenditure incurred ending 03/2022	2.50
Date of Start(Month/Yes)	Nov-21
Date of Completion(Month/Year)	Mar-22
No of Beneficiaries.	5000

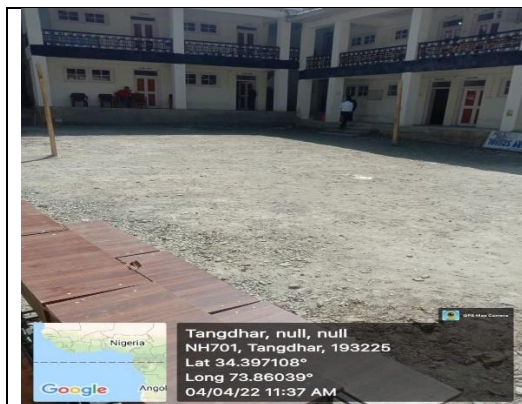

Sr .NO	178
Name of work with Location	Development of Playfield at GHSS TangdarKarnah by way of fencing
Department/Organisation	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Kupwara
AA Cost(Rs in Lakhs)	10.42
Total Cost of completion/Expenditure incurred ending 03/2022	2.00
Date of Start(Month/Yes)	Feb-22
Date of Completion(Month/Year)	Mar-22
No of Beneficiaries.	4000




Sr .NO	179
Name of work with Location	Development of Playfield at BHSS KukroosaHandwara by way of fencing
Department/Organisation	YSS/Directorate of YSS
Executive Agency	RDD
Block/District	Kupwara
AA Cost(Rs in Lakhs)	4.45
Total Cost of completion/Expenditure incurred ending 03/2022	2.99
Date of Start(Month/Yes)	Feb-22
Date of Completion(Month/Year)	Mar-22
No of Beneficiaries.	4500



S.No	180
Name of the work with location	Construction of Badminton Concrete Court at HSS Dangerpora
Department/Organization	YSS/Directorate of YSS
Executive Agency	Edu Deptt.
Block/District	Dangerpora
AA Cost (Rs. in Lakhs)	1.85
Total Cost of completion/Expenditure incurred ending 03/2022	1.85
Date of Start (Month/Year)	Sept,21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	1355



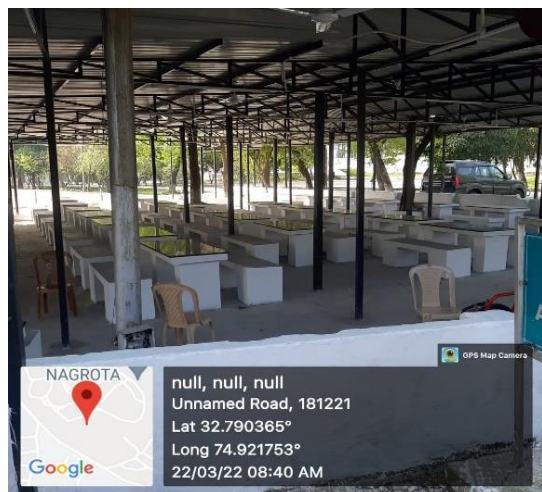

S.No	181
Name of the work with location	Construction of Concrete Badminton Court at Girls HSS Uri
Department/Organization	YSS/Directorate of YSS
Executive Agency	Edu Deptt.
Block/District	Uri
AA Cost (Rs. in Lakhs)	1.68
Total Cost of completion/Expenditure incurred ending 03/2022	1.60
Date of Start (Month/Year)	Nov, 21
Date of completion(Month/Year)	Mar-22
No. of beneficiaries	850





Sr.No.	182
Name of the work with Location	Cemented dinning table and benches in the dinning area of Cadet mess at CGN
Department/Organization	YSS/NCC Dte JK&L
Executive Agency	PWD
Block/District	Nagrota/Jammu
AA Cost (Rs. In lakhs)	5.00
Total Cost of Completion/Expenditure incurred ending 3/2022	3.40 (Work completed)
Date of Start (Month/Year)	Dec, 21
Date of Completion (Month/ year)	Mar,22
No. of beneficiaries	10000 Cdts





 <p>Azimuth: 61° (NE) Pitch: 5.7° (2.7') Time: 03-25-2022 13:55 Note: tiling of staff room stairs Powered by AngioCam</p>	Sr No	183
	Name of the work with Location	Tiling of staff room, stairs and complete electric fittings at NCC HQtrsSgr
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	8.29
	Total cost of Completion / Expenditure incurred ending 3/2022	4.47
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff

 <p>Azimuth: 120° (SE) Pitch: 6.8° (1.9') Time: 03-25-2022 13:52 Note: const. of guard room with toilets Powered by AngioCam</p>	Sr No	184
	Name of the work with Location	Construction of Guard room with toilet at NCC Group Srinagar
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	16.35
	Total cost of Completion / Expenditure incurred ending 3/2022	8.45
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff

 <p>Azimuth: 189° (S) Pitch: 32.4° (14.4') Time: 03-25-2022 14:00 Note: tiling of staff room at Powered by AngioCam</p>	Sr No	185
	Name of the work with Location	Tiling of Staff rooms in NCC Gp building ground floor NCC Group Headquarter Gogjibagh
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	2.77
	Total cost of Completion / Expenditure incurred ending 3/2022	1.50
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff

 <p>           Azimuth: 212° (SW)            Pitch: 28.3°            Time: 03-25-2022 13:59            Note: raised floor at staff room ncc            Powered by AngleCam         </p>	Sr No	186
	Name of the work with Location	Raising the floor of office at NCC Gp HQ Gogjibagh Srinagar
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	5.22
	Total cost of Completion / Expenditure incurred ending 3/2022	2.79
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff

 <p>           Azimuth: 263° (W)            Pitch: 8.0° (6.0°)            Time: 03-25-2022 14:04            Note: replacement of glaze            Powered by AngleCam         </p>	Sr No	187
	Name of the work with Location	Replacement of truss incl CGI roofing and inst. of New roof NCC Gp HQ Sgr
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	12.00
	Total cost of Completion / Expenditure incurred ending 3/2022	11.95
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff

 <p>           Azimuth: 318° (NW)            Pitch: 1.4° (1.9°)            Time: 03-25-2022 13:57            Note: construction of rifle stimulator room            Powered by AngleCam         </p>	Sr No	188
	Name of the work with Location	Construction of room for rifle stimulator at NCC Gp HQ Srinagar
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	PWD Division (R&B) Construction Div II
	Block / District	Srinagar
	AA Cost (Rs. Lakhs)	8.17
	Total cost of Completion / Expenditure incurred ending 3/2022	4.29
	Date of Start (Month / Year)	Oct 21
	Date of Completion (Month / Year)	Mar 22
	No of Beneficiaries	12650 Cdts& Staff





Sr No	189
Name of the work with Location	Construction/Renovation of Drainage system NCC Gp HQ Srinagar
Department / Organization	YSS/NCC Dte JK&L
Executive Agency	<b>Procurement</b>
Block / District	Srinagar
AA Cost (Rs. Lakhs)	1.44 lakhs
Total cost of Completion / Expenditure incurred ending 3/2022	1.44 lakhs
Date of Start (Month / Year)	Oct 21
Date of Completion (Month / Year)	Mar 22
No of Beneficiaries	12650 Cdts& Staff



S.No.	190
Name of the work with Location	Machinery equipment (NCC)
Department / Organization	YSS/NCC Dte JK&L
Executive Agency	Procurement through GEM Portal
Block / District	Jammu
AA Cost (Rs. Lakhs)	10.00lakh
Total cost of Completion / Expenditure incurred ending 3/2022	9.66 LAKH
Date of Start (Month / Year)	Oct, 21
Date of Completion (Month / Year)	Mar, 22
No of Beneficiaries	12650 cadets



	Sr No	191
	Name of the work with Location	Matresses = 300 NCC camping Ground Nagrota
	Department / Organization	YSS/NCC Dte JK&L
	Executive Agency	Procurement through GEM Portal
	Block / District	Jammu
	AA Cost (Rs. Lakhs)	5.98 lakh
	Total cost of Completion / Expenditure incurred ending 3/2022	6.00
	Date of Start (Month / Year)	Oct, 21
	Date of Completion (Month / Year)	Mar, 22
	No of Beneficiaries	12650 cadets

	Sr No	192
	Name of the work with Location	500 Chairs NCC camping Ground Nagrota
	Department / Organization	YSS/NCC Dte JK&L
	Block / District	Jammu
	AA Cost (Rs. Lakhs)	4.00 lakh
	Total cost of Completion / Expenditure incurred ending 3/2022	3.99 lakh
	No. of Beneficiaries	12650 cadets
